

STCP 19-2 Issue 0043 Construction Process & Scheme Closure

STC Procedure Document Authorisation

Company Party	Name of Party Representative	Signature	Date
National Grid Electricity Transmission plc			
SP Transmission Ltd			
Scottish Hydro-Electric Transmission Ltd			
Offshore Transmission Owners			

STC Procedure Change Control History

Issue 001	16/03/2005	BETTA Go-Live version
Issue 002	26/05/2005	Issue 002 incorporating PA016
Issue 003	25/10/2005	Issue 003 incorporating PA034 & PA037
Issue 004	24 xx/11/2009	Issue 004 incorporating changes for offshore

1 Introduction

1.1 Scope

1.1.1 This document applies to the construction process and the following aspects of the Scheme closure process in the authorised areas of TOs:

- the closure of a Scheme when a Connection is commissioned or construction is completed;
- the termination of a TO Construction Agreement; and/or
- the termination of a Bilateral Agreement.

1.1.2 For the purposes of this document, the TOs are:

- SPT; ~~and~~
- SHETL; and
- All Offshore Transmission Licence holders as appointed by Ofgem from time to time. -

1.2 Objective

1.2.1 The objective of this document is to provide detailed processes for:

- construction, modification or replacement of Connection assets;
- construction, modification or replacement of infrastructure assets related to a new or modified Connection;
- construction, modification or replacement of infrastructure assets not related to a new or modified Connection;
- One Off Works;
- closure of Schemes when a Connection is commissioned or construction of Connection assets is completed;
- the termination of a TO Construction Agreement;
- the termination of a Bilateral Agreement; and,
- the process to be followed when arranging for the Disconnection and removal of the relevant TO Connection assets following the termination of a Bilateral Agreement and/or TO Construction Agreement.

1.2.2 This document details certain interactions between NGET and each TO in the construction of new or modified Transmission assets or the replacement of Transmission assets. The document also sets out some of the actions to be taken upon the termination of a Bilateral Agreement and/or TO Construction Agreement.

2 Key Definitions

2.1 For the purposes of STCP 19-2:

2.1.1 **Detailed TO Construction Programme** is as defined in Paragraph 5.2.1.3.

2.1.2 **Disconnection Notice Programme** is the programme to manage the Disconnection notice process and will be included with the TO Termination Notices. The Disconnection Notice Programme shall list the key milestones that shall be completed as the Disconnection is progressed. The dates of these milestones shall be agreed by all Parties.

2.1.3 **Disconnection Steering Group** means a team made up of named representatives from NGET and the Affected Parties, formed to oversee the Disconnection. The members of the Disconnection Steering Group shall be identified on the Scheme Briefing Notes. The remit of this group is to agree the dates within the Disconnection Notice Programme, monitor progress and agree any changes.

- 2.1.4 **Final Project Report** is a report produced by a TO on completion of a Scheme and includes the information specified in section 7.3.2 of this STCP.
- 2.1.5 **Infrastructure Construction Project** is that construction project entered into as a result of Works undertaken pursuant to STCP 16-1: Investment Planning.
- 2.1.6 **Initial Project Meeting** is the meeting called by the relevant TO as soon as reasonably practicable following the signing of a TO Construction Agreement by all of the Parties or as detailed in the relevant Project Listing Document. NGET and each TO shall be entitled to attend such meeting and any other attendees as agreed between the relevant Parties.
- 2.1.7 **Post Project Review** means a review of a Scheme undertaken by the Joint Project Parties upon the completion of a Scheme.
- 2.1.8 **Reporting Date(s)** are those dates (if any) set out in the Detailed TO Construction Programme for the production of reports required throughout the Detailed TO Construction Programme.
- 2.1.9 **Scheme** means the TO Construction Works relating to a specific TO Construction Agreement.
- 2.1.10 **Site Access Date(s)** are those dates that may be contained within the Detailed TO Construction Programme by which a TO requires access to a Connection Site in order to complete Transmission Connection Asset Works or Transmission Reinforcement Works in accordance with the Detailed TO Construction Programme.
- 2.1.11 **Stage-by-Stage Document** is that document produced in accordance with Section 5.4 or Section 6.4, as the case may be, of this STCP.
- 2.1.12 **Stage Date(s)** are those dates that may be contained within the Detailed TO Construction Programme by which each individual stage of a Detailed TO Construction Programme shall be completed, or the date upon which a scheduled payment detailed within the Detailed TO Construction Programme becomes due.
- 2.1.13 **Termination Notice** a notice sent by, in the case of NGET, to each relevant TO upon the termination of a Bilateral Agreement or, in the case of a TO, to NGET upon the termination of a TO Construction Agreement.
- 2.1.14 **Termination Report** is a report produced by the relevant TO, giving details pertinent to closure upon termination of a Bilateral Agreement or a TO Construction Agreement.
- 2.1.15 **TO Construction Project** is a construction project undertaken by a TO pursuant to a TO Construction Agreement.
- 2.1.16 **TO Infrastructure Construction Programme** is as defined in Section 6.2.
- 2.1.17 **Transmission Infrastructure Assets** are those TO assets not classed as Transmission Connection Assets.
- 2.1.18 **Transmission Infrastructure Works** are those Works undertaken pursuant to STCP16-1: Investment Planning.

3 General Provisions

3.1 Nuclear Site Licence Provisions Agreement

- 3.1.1 When following this process where this may interact with, impact upon or fall within the boundary of a Nuclear Site Licence holder's site, or may otherwise have any form of affect and/or implication for a nuclear power station consideration must be given to the relevant provisions of the applicable Nuclear Site Licence Provisions Agreement, the CUSC Bilateral Connection Agreement for that site, paragraph 6.9.4 of the CUSC and Section G3 of the STC to ensure compliance with all of these obligations.

4 Construction Process

4.1 Introduction

4.1.1 The construction process may be triggered either through a legally binding Acceptance of a TO Construction Agreement (“TOCA”) or Indemnity Agreement by NGET , or through detailed option development within Investment Planning STCP 16-1.

4.2 Commencement

4.2.1 The following activities shall commence with the triggers set out in the following table:

Trigger	Activity
(A) Legally binding Acceptance of TO Construction Agreement (“TOCA”) by NGET .	Construction of new Transmission Connection Assets, associated infrastructure and One Off Works in accordance with the TOCA.
	Construction works to modify or replace Transmission Connection Assets in accordance with the TOCA.
	Construction, modification or replacement of Transmission Infrastructure Assets triggered by a new or modified Connection in accordance with the TOCA.
(B) Detailed option development within Investment Planning STCP 16-1	Construction, modification or replacement of Transmission Infrastructure Assets not triggered by a new or modified Connection

4.2.2 The process followed resulting from Trigger A is set out in Section 5 of this STCP.

4.2.3 The process followed resulting from Trigger B is set out in Section 6 of this STCP.

5 Construction Projects

5.1.1 The Construction Project includes the following stages:

- commencement;
- preparation and consideration of Detailed TO Construction Programmes;
- applying for planning Consents;
- preparation and consideration of Stage-by-Stage documents;
- provision of drawings;
- progress reporting and information exchange;
- TO Final Sums reporting; and
- completion.

5.1.2 As soon as possible following receipt of an executed copy of the relevant TO Construction Agreement (“TOCA”), the relevant TO will arrange the Initial Project Meeting. The Initial Project Meeting shall be attended by NGET –and the other affected TO and by any other parties as agreed between the relevant TO, NGET and the other affected TO. The objective of the Initial Project Meeting shall be:

- to perform a high-level review of the TO Construction Project;
- to agree a timetable for the production of a Detailed TO Construction Programme;
- to discuss indicative Outage requirements; and
- for each Party to confirm their principle contact for the TO Construction Project.

5.2 TO Construction Programme

5.2.1 Preparation of a Detailed TO Construction Programme

5.2.1.1 The relevant TO shall prepare a Detailed TO Construction Programme in accordance with the timetable agreed at the Initial Project Meeting.

5.2.1.2 The Detailed TO Construction Programme shall be compliant with the TO Construction Agreement(s) and shall contain any other relevant information as notified by NGET – to a TO in accordance with the STC.

5.2.1.3 The- Detailed TO Construction Programme shall contain, where applicable:

- planning permission application dates;
- date for the provision of the Stage-by Stage Document by the relevant TO to NGET
- dates by when Consents are required;
- dates by when any leases or licenses are required;
- dates by when the TO needs certain information from the User;
- dates for provision of drawings to NGET ;
- Site Access Date;
- Stage Dates;
- Commissioning Programme Commencement Dates;
- Completion Dates; and,
- Reporting Dates.

Such dates shall be consistent with the STC and TOCA where applicable.

5.2.1.4 The Detailed TO Construction Programme may be amended from time to time by the relevant TO after discussion with, and with the consent of, the Joint Project Parties. Upon any such amendment an updated Detailed TO Construction Programme shall be provided to NGET and NGET shall provide such to the Joint Project Parties.

5.2.2 NGET's consideration of the Detailed TO Construction Programme

5.2.2.1 NGET- may discuss the Detailed TO Construction Programme with any relevant User. The TOs shall provide all reasonable assistance to answer any queries raised by a User and shall accommodate a request for a meeting at the convenience of all relevant parties.

5.2.2.2 If any of the Joint Project Parties identify any reasons why the Detailed TO Construction Programme is, in its reasonable opinion, inappropriate, such Joint Project Party shall submit such views to the other Joint Project Parties in writing; providing clear reasons as to why the Detailed TO Construction Programme is not appropriate. The relevant TO shall either redraft the Detailed TO Construction Programme reflecting any views put forward and/or proceed with the works as laid out in the Detailed TO Construction Programme to ensure that the TO(s) meet the Completion Date set out in the TOCA(s).

5.3 Obtaining Consents

5.3.1 Where requested by a TO, NGET- shall provide all reasonable support for that TO's application for Consents.

5.3.2 NGET -shall be entitled to its reasonable costs from the TO(s) in providing such support. In particular, NGET shall provide:

- justification of any generation or Demand backgrounds which underpin the need for a reinforcement;
- evidence on ongoing System operation costs; or,
- details of the Connection requirements (as the counterparty to the agreement with any User).

5.3.3 NGET -shall inform the TO(s) when all relevant Consents have been obtained by the User(s). The TO shall inform NGET- when they have obtained all Consents in respect of a TO Construction Agreement.

5.4 Stage-by-Stage Document

5.4.1 TO preparation of a Stage-by-Stage Document

5.4.1.1 The TO(s) shall provide NGET -with the Stage-by-Stage Document in accordance with the Detailed TO Construction Programme.

5.4.1.2 The purpose of the Stage-by-Stage Document is to set out the TO(s) fundamental approach to the work. Text in reasonable detail shall be included in the Stage-by-Stage Document to describe the key activities to be undertaken at each stage. The Stage-by-Stage Document shall set out for each stage:

- assets which are live;
- assets which are dead; and
- assets which are being worked on.

5.4.1.3 Details of any contingency arrangements relating to the operation of the System concerning each stage of the Transmission Construction Works shall be determined by the TO(s) and shall be contained in the Stage-by-Stage Document.

5.4.1.4 The assets to be commissioned, or re-commissioned, after each stage of the Transmission Construction Works is complete shall be determined by the TO(s) and shall also be set out in the Stage-by-Stage Document.

5.4.2 NGET's consideration of the Stage-By-Stage Document and Outage requirements

5.4.2.1 NGET shall review the Stage-by-Stage Document and agree the Outage requirements received from the TO(s) in accordance with STCP 11-1 Outage Planning.

- 5.4.2.2 Where appropriate, NGET –shall be responsible for liaising with relevant Users regarding the Stage-by-Stage Document or the Outage requirements.
- 5.4.2.3 If any of the Joint Project Parties identify any reasons why the Stage-by-Stage Document is, in its reasonable opinion, inappropriate, such Joint Project Party shall submit such views to the other Joint Project Parties in writing; providing clear reasons as to why the Stage-by-Stage Document is not appropriate. The relevant TO shall either redraft the Stage-by-Stage Document reflecting any views put forward and/or proceed with the works as laid out in the Stage-by-Stage Document to ensure that the TO(s) meet the Completion Date set out in the TOCA(s).

5.5 Drawings to be provided

- 5.5.1 The procedure to be followed for the exchange, development and signing off of technical and non-technical documents and drawings required throughout the construction process are detailed in STCP 19-4 Commissioning & Decommissioning.

5.6 Progress Reporting and information exchange

- 5.6.1 The Joint Project Parties shall liaise throughout the Transmission Construction Works and each shall provide to the other any information the other reasonably requires in order to assist each other in the works. In the case of NGET–, this shall include the provision of all information reasonably requested by the TO(s) (whether held by NGET –or a User) to enable the TO(s) to complete the Transmission Construction Works. In the case of the TO(s), this shall include the provision of all information reasonably requested by NGET– in order that NGET –fulfils its obligations to the User.
- 5.6.2 The TO(s) shall provide to NGET– reports on a monthly basis (or other timetable as agreed between the TO(s) and NGET) in respect of Consents progress and expenditure in the format laid out in Appendix B: Consents Reporting Pro-Forma: (or such other format as agreed between the relevant TO and NGET). The dates for submission of these reports shall be included in the Detailed TO Construction Programme submitted to NGET by the relevant TO, and shall be no later than 5 Business Days before the end of that calendar month (or other time as agreed between the TO(s) and NGET).
- 5.6.3 The TO(s) shall provide on a quarterly basis (or other timetable as agreed between the TO(s) and NGET) reports in the format laid out in Appendix C: Quarterly Reporting Pro Forma (or other format as agreed between the relevant TO and NGET). The dates for submission of these reports shall be included in the Detailed TO Construction Programme, and shall be no later than [7] Business Days before the end of that Calendar Quarter (or other time as agreed between the TO(s) and NGET).
- 5.6.4 NGET –and the TO(s) shall, unless otherwise agreed, each provide representation at site meetings to be held on dates set out in the Detailed TO Construction Programme.
- 5.6.5 When considering the scheduling of meetings, the provision of data and/or the timetable for providing reports, due regard must be given to any confidentiality restrictions laid out in the STC.

5.7 TO Final Sums Reporting

- 5.7.1 The TO(s) shall provide TO Final Sums reporting in the format set out in Appendix D, in accordance with the terms of the TO Construction Agreement.

5.8 Complete construction works

- 5.8.1 Each TO shall complete the works in accordance with the Detailed TO Construction Programme and the Stage-by-Stage Document.
- 5.8.2 Where it is recognised, at any stage during the works, by the Joint Project Parties, that the timetable for the completion of the works contained within the Stage-by-Stage Document may no longer be feasible, then the Detailed TO Construction Programme shall be reassessed by the Joint Project Parties and re-issued by the TO(s), along with an updated Stage-by-Stage document, if appropriate.

6 Investment Planning Construction Programme

6.1 Introduction

6.1.1 The Infrastructure Construction Project includes the following stages:

- Commencement
- preparation and consideration of TO Infrastructure Construction Programmes;
- applying for planning Consents;
- preparation and consideration of Stage-by-Stage Documents;
- provision of drawings;
- information exchange; and
- completion.

6.1.2 As soon as reasonably practicable following detailed option development within Investment Planning STCP16-1, the relevant TO will arrange the Initial Project Meeting. The objective of the Initial Project Meeting shall be:

- to perform a high-level review of the Infrastructure Construction Project;
- to develop a timetable for the production of a detailed TO Infrastructure Construction Programme; and
- to discuss indicative Outage requirements.

6.2 TO Infrastructure Construction Programme

6.2.1 The relevant TO shall prepare a TO Infrastructure Construction Programme in accordance with the timetable agreed at the Initial Project Meeting and shall supply a copy of the TO Infrastructure Construction Programme to NGET.

6.2.2 ~~The TO~~The TO Infrastructure Construction Programme shall contain, where applicable:

- planning permission application dates;
- date for the provision of the Stage-by Stage Document
- dates by when Consents are required;
- dates by when any leases or licenses are required;
- dates for provision of drawings to NGET ;
- Stage Dates;
- Commissioning Programme Commencement Dates; and,
- Completion Dates.

6.2.3 The ~~TO~~ TO Infrastructure Construction Programme may be amended from time to time by the relevant TO and the TO shall supply upon reasonable request by NGET a copy of such amended TO Infrastructure Construction Programme(s). NGET may make such request at the Initial Project Meeting.

6.2.4 NGET 's Consideration of the TO Infrastructure Construction Programme

6.2.4.1 NGET ~~may~~ discuss the TO Infrastructure Construction Programme with any relevant User. The TOs shall provide all reasonable assistance to answer any queries raised by a User and shall accommodate a request for a meeting at the convenience of all relevant parties.

6.2.4.2 If NGET ~~and/or~~ any TO and/or any User impacted by the TO Infrastructure Construction Programme identify any reasons why the TO Infrastructure Construction Programme is, in its reasonable opinion, inappropriate, NGET and/or the TO impacted by the TO Infrastructure Construction Programme shall submit such views to the TO in writing, providing clear reasons as to why the TO Infrastructure Construction Programme is not appropriate. The TO shall either redraft the detailed TO Infrastructure Construction Programme reflecting any views put forward and/or proceed with the works as laid out in the detailed TO Infrastructure Construction Programme.

6.3 Obtaining Consents

- 6.3.1 Where requested by a TO, NGET -shall provide all reasonable support for that TO's application for Consents.
- 6.3.2 NGET -shall be entitled to its reasonable costs from the TO(s) in providing such support. In particular, NGET shall provide:
- justification of any generation or Demand backgrounds which underpin the need for a reinforcement; or,
 - evidence on ongoing System operation costs;

6.4 Stage-by-Stage Document

6.4.1 TO preparation of a Stage-by-Stage Document

- 6.4.1.1 The TO(s) shall provide NGET- with the Stage-by-Stage Document in accordance with the TO Infrastructure Construction Programme. The Stage-by-Stage Document shall set out the proposals in reasonable detail for each stage of the Transmission Infrastructure Works.
- 6.4.1.2 The purpose of the Stage-by-Stage Document is to set out the TO(s) fundamental approach to the work. Text in reasonable detail shall be included in the Stage-by-Stage Document to describe the key activities to be undertaken at each stage. The Stage-by-Stage Document shall set out for each stage:
- assets which are live;
 - assets which are dead; and
 - assets which are being worked on.
- 6.4.1.3 Details of any contingency arrangements relating to the operation of the System concerning each stage of the Transmission Infrastructure Works shall be determined by the TO(s) and shall be contained in the Stage-by-Stage Document.
- 6.4.1.4 The assets to be commissioned, or re-commissioned, after each stage of the Transmission Infrastructure Works is complete shall be determined by the TO(s) and shall also be set out in the Stage-by-Stage Document.

6.4.2 NGET 's consideration of the Stage-by-Stage Document and Outage requirements

- 6.4.2.1 NGET- shall review the Stage-by-Stage Document and agree the Outage requirements received from the TO(s) in accordance with STCP 11-1 Outage Planning.
- 6.4.2.2 If any of the Joint Project Parties identify any reasons why the Stage-by-Stage Document is, in its reasonable opinion, inappropriate, such Joint Project Party shall submit such views to the other Joint Project Parties in writing; providing clear reasons as to why the Stage-by-Stage Document is not appropriate. The relevant TO shall either redraft the Stage-by-Stage Document reflecting any views put forward and/or proceed with the works as laid out in the Stage-by-Stage Document to ensure that the TO(s) meet the Completion Date set out in the TO Infrastructure Construction Programme(s)

6.5 Drawings to be provided

6.5.1 The procedure to be followed for the exchange, development and signing off of technical and non-technical documents and drawings required throughout the construction process are detailed in STCP 19-4 Commissioning & Decommissioning.

6.6 Information Exchange

6.6.1 NGET and the TO(s) shall liaise throughout the Transmission Infrastructure Works and each shall provide to the other any necessary progress information the other reasonably requires in order to assist each other in the works.

6.7 Complete construction works

6.7.1 Each TO shall complete the works in accordance with the detailed TO Infrastructure Construction Programme and the Stage-by-Stage Document.

6.7.2 Where it is recognised, at any stage during the works, by the TO(s) or NGET, that the timetable for the completion of the works contained within the Stage-by-Stage Document may no longer be feasible, then the detailed TO Infrastructure Construction Programme shall be reassessed by the TO(s) and NGET and re-issued by the TO(s), along with an updated Stage-by-Stage Document, if appropriate.

7 Post TOCA Completion Date Activities

7.1 Termination Amounts Reporting

7.1.1 Following the Completion Date of a Construction Project, each TO shall provide NGET- no less than 82 calendar days prior to 31st March and 30th September of each year with an estimate of all payments which may be required to be paid by NGET in respect of Termination Amounts for the six-month period commencing from 31st March and 30th September (such charges to be in accordance with the relevant TO Charging Statement). The return shall be in the format laid out in Appendix F: Termination Amounts Reporting. In addition, the TO(s) shall provide to NGET- all information and explanations needed by NGET in order to answer any queries raised by a User on such estimates.

7.2 Closure

7.2.1 Following the Completion Date of a Construction Project and/or termination of a Construction Agreement, Schemes need to be formally closed and the final construction costs identified and provided within timescales agreed between the relevant Parties, but in any event within 12 months.

7.2.2 On completion of a Scheme, the closure process in section 7.3 shall be followed in the case of firm price agreements, with the exception that TO charges do not need to be calculated.

7.2.3 Termination of a Construction Agreement before completion may give rise to TO Final Sums and termination of a Bilateral Agreement after commissioning may give rise to Termination Amounts. In both circumstances a closure process will need to be carried out and these are covered in this procedure.

7.3 Closure upon completion of Scheme

7.3.1 Within 2 months of the Completion Date (in the TO Construction Programme), where either party to a TOCA considers it necessary, such parties shall arrange a Post Project Review to consider the proposed contents of the Final Project Report including any learning points.

7.3.2 Within 8 months of the Completion Date (or as otherwise agreed), the TO shall send NGET a Final Project Report which shall contain the following, where appropriate:

- a signed statement from the TO(s) to the effect that all costs have been accounted for and that no further scheduled or planned financial payments are due under the TO(s) Construction Agreement and as at the date thereof, no financial claim has been made in respect of any other matter pertaining to the Scheme;
- whether there are any outstanding works;

- finalised schedules of data, as identified in Appendix E: Scheme Outturn Charge Notification
- lessons learned impacting on the NGET /TO interface;
- variance analysis of finalised schedules of data against the latest schedules provided to NGET ; and
- confirmation by the TO(s) of the addition of appropriate data for the Works to the Connection Site Specification and Services Capability Specification.

7.3.3 NGET- shall check the contents of the Final Project Report. If required, NGET shall request further detail/clarification from a TO, specifying a reasonable response time and details of the query.

7.3.4 The relevant TO shall supply the further detail or clarification regarding the contents of the Final Project Report if requested by NGET-.

7.3.5 Where a User has a query concerning the outturn charges based upon those figures provided in the Final Project Report, the process set out in the STCP 14-3 Customer Charging Queries, shall be followed.

7.3.6 When the closure process has been completed NGET -shall notify the TO(s) and confirm NGET 's acceptance of the Final Project Report.

7.3.7 In the event that NGET -has over/underpaid given the figures in the Final Project Report, the relevant TO shall submit a reconciling invoice to NGET .

7.3.8 NGET -shall check the reconciling invoice and settle any outstanding sums in accordance with STCP 13-1 Invoicing and Payment.

7.4 Closure upon termination of a TO Construction Agreement

7.4.1 Following the termination of a TO Construction Agreement the TO shall send NGET -an update of outstanding contents and Final Sums and a Termination Report in accordance with the provisions of the TO Construction Agreement.

7.4.2 On receipt of the Termination Report, NGET -shall check the data. NGET -may request further detail or clarification from the TO(s) regarding the Termination Report if required.

7.4.3 Upon request by NGET the TO(s) shall supply further detail or clarification regarding the Termination Report if required and shall notify NGET of any updates to the previously notified TO Final Sums and/or outstanding Consents.

7.4.4 As soon as reasonably practicable, and in any case within 6 months of the termination of the TO(s) Construction Agreement, the TO(s) shall provide NGET with a statement of TO Final Sums together with evidence of such costs having been incurred and/or paid, and/or having been committed to be incurred including any interest thereupon. The TO(s) shall also provide a statement signed on behalf of the TO(s) to confirm that all costs have been accounted for and that no further scheduled or planned financial payments are due under the TO(s) Construction Agreement and as at the date thereof, no financial claim has been made in respect of any other matter pertaining to the Scheme.

7.5 Closure upon termination of a Bilateral Agreement

7.5.1 Within 2 Business Days of:

- NGET receiving notice from a User that the User intends to terminate, Disconnect or partially Disconnect the User Equipment which is connected to a TO's Transmission System; or
- NGET giving notice of termination to the User

The NGET -Lead Person shall issue a notice of termination in the form of a Scheme Briefing Note ("SBN") (see STCP18-1 Connection and Modification Application, Appendix B.1) to each Affected Party's Named Contact. The SBN shall include (where appropriate):

- a copy of the User's notice to terminate and/or Disconnect or a copy of NGET notice of termination;

- the date of termination;
 - the draft Disconnection Notice Programme dates entered by NGET ; and
 - details of the Disconnection, identifying the Host TO, Affected TO(s) and Other Affected TO(s) as appropriate, the NGET Lead Person and a NGET Scheme number.
- 7.5.2 If the User gives NGET -more than six months notice of termination, NGET shall only inform the Affected Parties of the User's wish to Disconnect with the User's consent. Should a User withhold its consent then NGET- shall notify the Affected Parties six months prior to the date at which the User wishes to Disconnect.
- 7.5.3 Within 2 Business Days of receipt of an SBN from NGET–, each Affected Party shall acknowledge receipt of such SBN to the NGET Lead Person by email, and shall advise NGET of the identity of that Affected Party's Lead Person. The NGET –Lead Person shall update the SBN with details of each Affected Party's Lead Person. All formal communication related to the termination shall be addressed to the appropriate Lead Person, who shall be the TO's representative on the Disconnection Steering Group.
- 7.5.4 The NGET -Lead Person and each Affected Party's Lead Person shall agree a date to meet and discuss the Disconnection Notice Programme. NGET -shall update the SBN to record this date. This meeting may be cancelled if the Parties agree that it is not required.
- 7.5.5 As soon as reasonably possible, but in any event within 2 Business Days of sending the SBN to each Affected Party, the NGET Lead Person shall confirm the latest version of the Planning Assumptions to be used by the Affected Parties in assessing the termination. The Host TO shall determine which Connection assets may be redundant as a result of the User's notice to Disconnect or NGET-'s notice of termination to the User.
- 7.5.6 Following receipt of the confirmation of the Planning Assumptions to be used in assessing the termination from NGET–, each Affected Party shall take into account the Planning Assumptions when considering any implications on the draft Disconnection Notice Programme.
- 7.5.7 The dates within the Disconnection Notice Programme shall be agreed by the NGET– Lead Person and each Affected Party's Lead Person within 10 Business Days of receipt by the Affected Parties of the SBN. Any proposed amendments to the Disconnection Notice Programme shall be submitted to the NGET –Lead Person at least one Business Day prior to any meeting of the Disconnection Steering Group.
- 7.5.8 In accordance with the agreed Disconnection Notice Programme and prior to the Termination Date, Affected TO(s) shall prepare and issue a Termination Report to the NGET- Lead Person.
- 7.5.9 The Termination Report shall contain the following details where appropriate:
- the estimated cost of removal of equipment/Disconnection/storage, the estimated cost of making good the condition of the site, or estimate of any other cost associated with the termination, and shall provide as soon as practicable, evidence of such costs having been incurred;
 - assets in respect of which a Termination Amount is payable, which are re-used at the same Connection Site or elsewhere in the ~~GB~~-National Electricity Transmission System, including infrastructure assets;
 - assets in respect of which a Termination Amount is payable which are disposed or made redundant as a result of the Disconnection;
 - any outstanding works with a programme for their completion;
 - consideration of the effect on other agreements (e.g. Interface Agreement, rental agreement, lease agreement, wayleave agreement);
 - timescales for the Disconnection and removal of assets;
 - de-commissioning timescales;
 - environmental and consents issues;
 - impact on other customers and Third Party Works (the NGET Lead Person to establish the requirements of any remaining connected customers); and,
-

- consideration of removal of communications.
- 7.5.10 If there is a requirement to reinforce a TO's Transmission System as a result of the notice to Disconnect then this infrastructure reinforcement shall be identified in accordance with STCP 16-1 Investment Planning.
- 7.5.11 NGET –shall check the contents of the Termination Report and shall request further detail/clarification from the Affected Parties if required. NGET– and the Affected Parties shall meet to discuss the Disconnection where required by NGET . The NGET– Lead Person may request an updated Termination Report from an Affected Party to reflect any agreed changes resulting from such discussions. Upon such a request the Affected Parties shall provide to the NGET Lead Person the requested updated Termination Report as soon as reasonably practicable and no later than the Termination Date.
- 7.5.12 NGET –and Affected TO(s) shall liaise to discuss indicative Outage requirements (in accordance with STCP 11-1 Outage Planning and endeavouring to meet the User's Disconnection date) and agree which assets (if any) should be removed from the System.
- 7.5.13 Following submission of the final Termination Report to NGET–, the TO:
- shall calculate the Termination Amounts (in accordance with that TO's Charging Methodology); and
 - invoice NGET for such Termination Amounts.
- 7.5.14 NGET –shall settle any Termination Amounts pursuant to section 7.5.13 in accordance with STCP 13-1 Invoicing and Payment.

7.6 Termination Amounts – Re-use


- 7.6.1 This section 7.6 deals with issues relating to re-use of TO(s) assets in respect of which Termination Amounts have been paid by NGET–.
- 7.6.2 The TO(s) shall use reasonable endeavours to re-use assets where Termination Amounts have been paid. If at any point, the TO(s) re-use or dispose of any of the assets contained in the Termination Report, they shall immediately inform NGET–. In the event that a Termination Amount has been paid in respect of assets and the TO subsequently re-uses such assets, that TO shall pay to NGET– the net asset value of such asset.
- 7.6.3 Upon request in writing, at the cost of NGET , and no more frequently than once each calendar year, the TO(s) shall issue a certificate indicating whether or not such assets have been re-used. If, at any time, the TO(s) decide that it is not economic to retain any Plant or Apparatus constituting any asset in respect of which Termination Amounts have been paid it may, at its reasonable discretion, dispose of the said Plant and/or Apparatus and pay NGET any sums due based on the net asset value of such asset.


7.7 Disconnection

- 7.7.1 The Host TO shall give, and NGET –shall procure that any relevant User gives, such rights to access land as are reasonably required in order to facilitate the removal of the User's Equipment and Host TO's assets on each other's land.
- 7.7.2 The Host TO assets shall be physically Disconnected and removed from the Transmission System in accordance with STCP 19-4, Commissioning & Decommissioning.


Appendix A: Process Diagrams


Note that the Process Diagrams shown in this Appendix A are for information only. In the event of any contradiction between the process represented in this Appendix and the process described elsewhere in this STCP, then the text elsewhere in this STCP shall prevail.

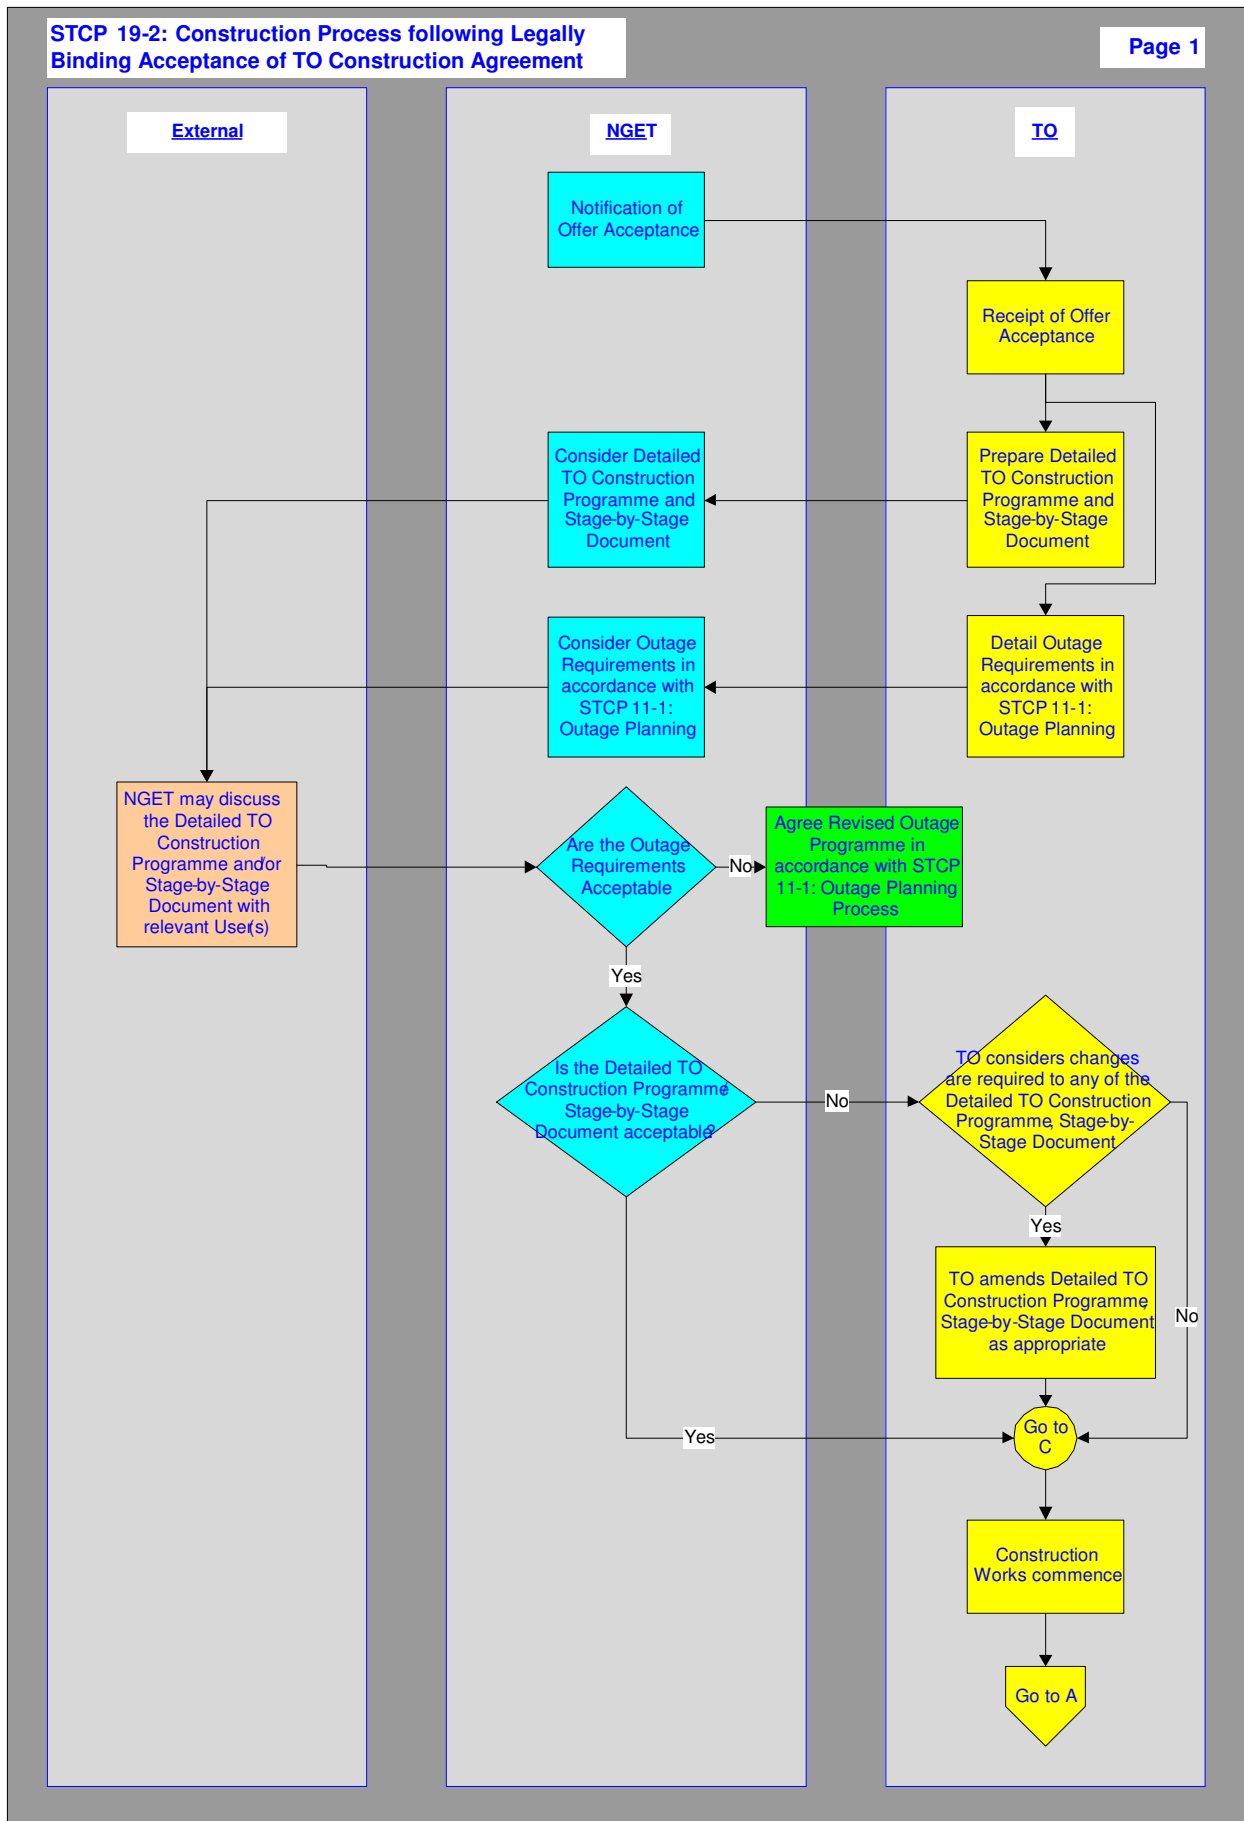


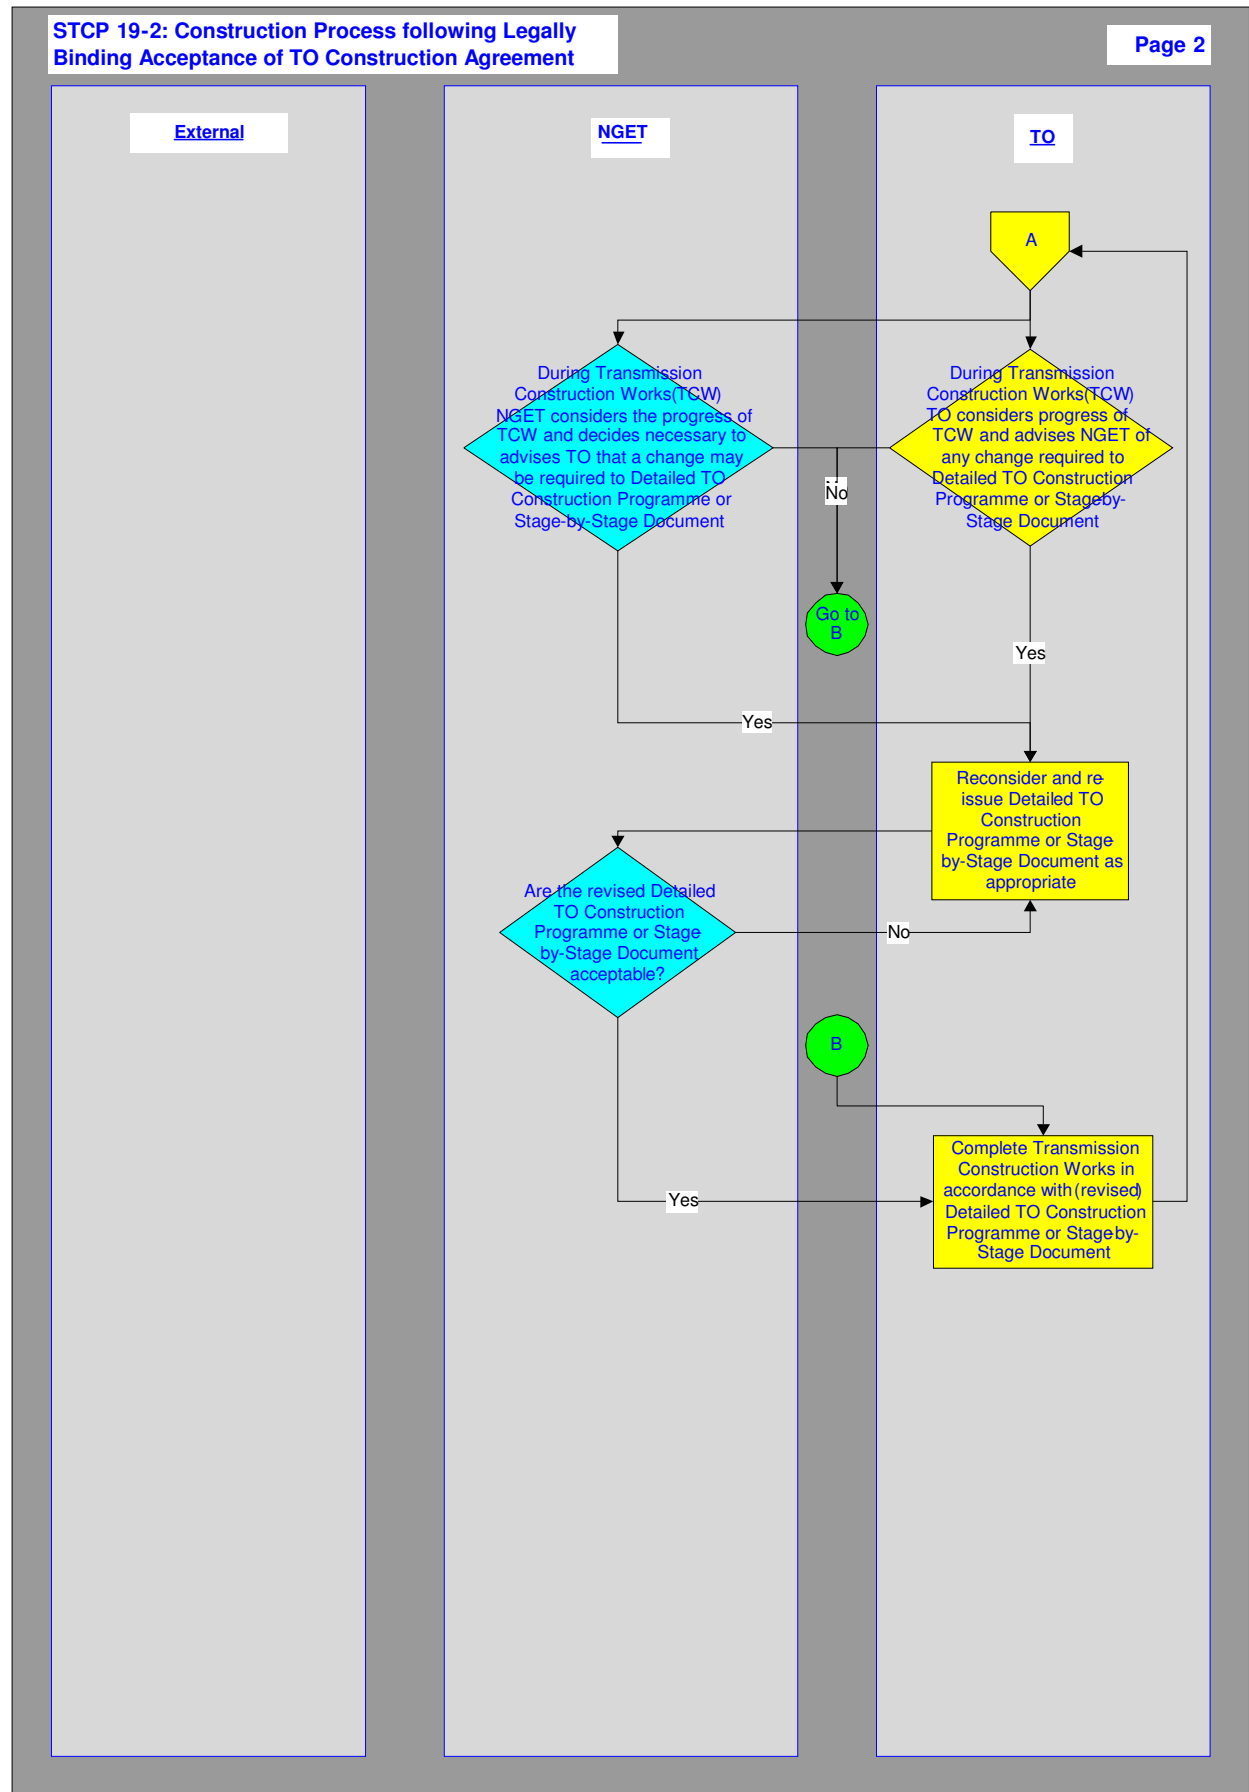



STCP 19-2: Construction Process following Legally Binding Acceptance of TO Construction Agreement

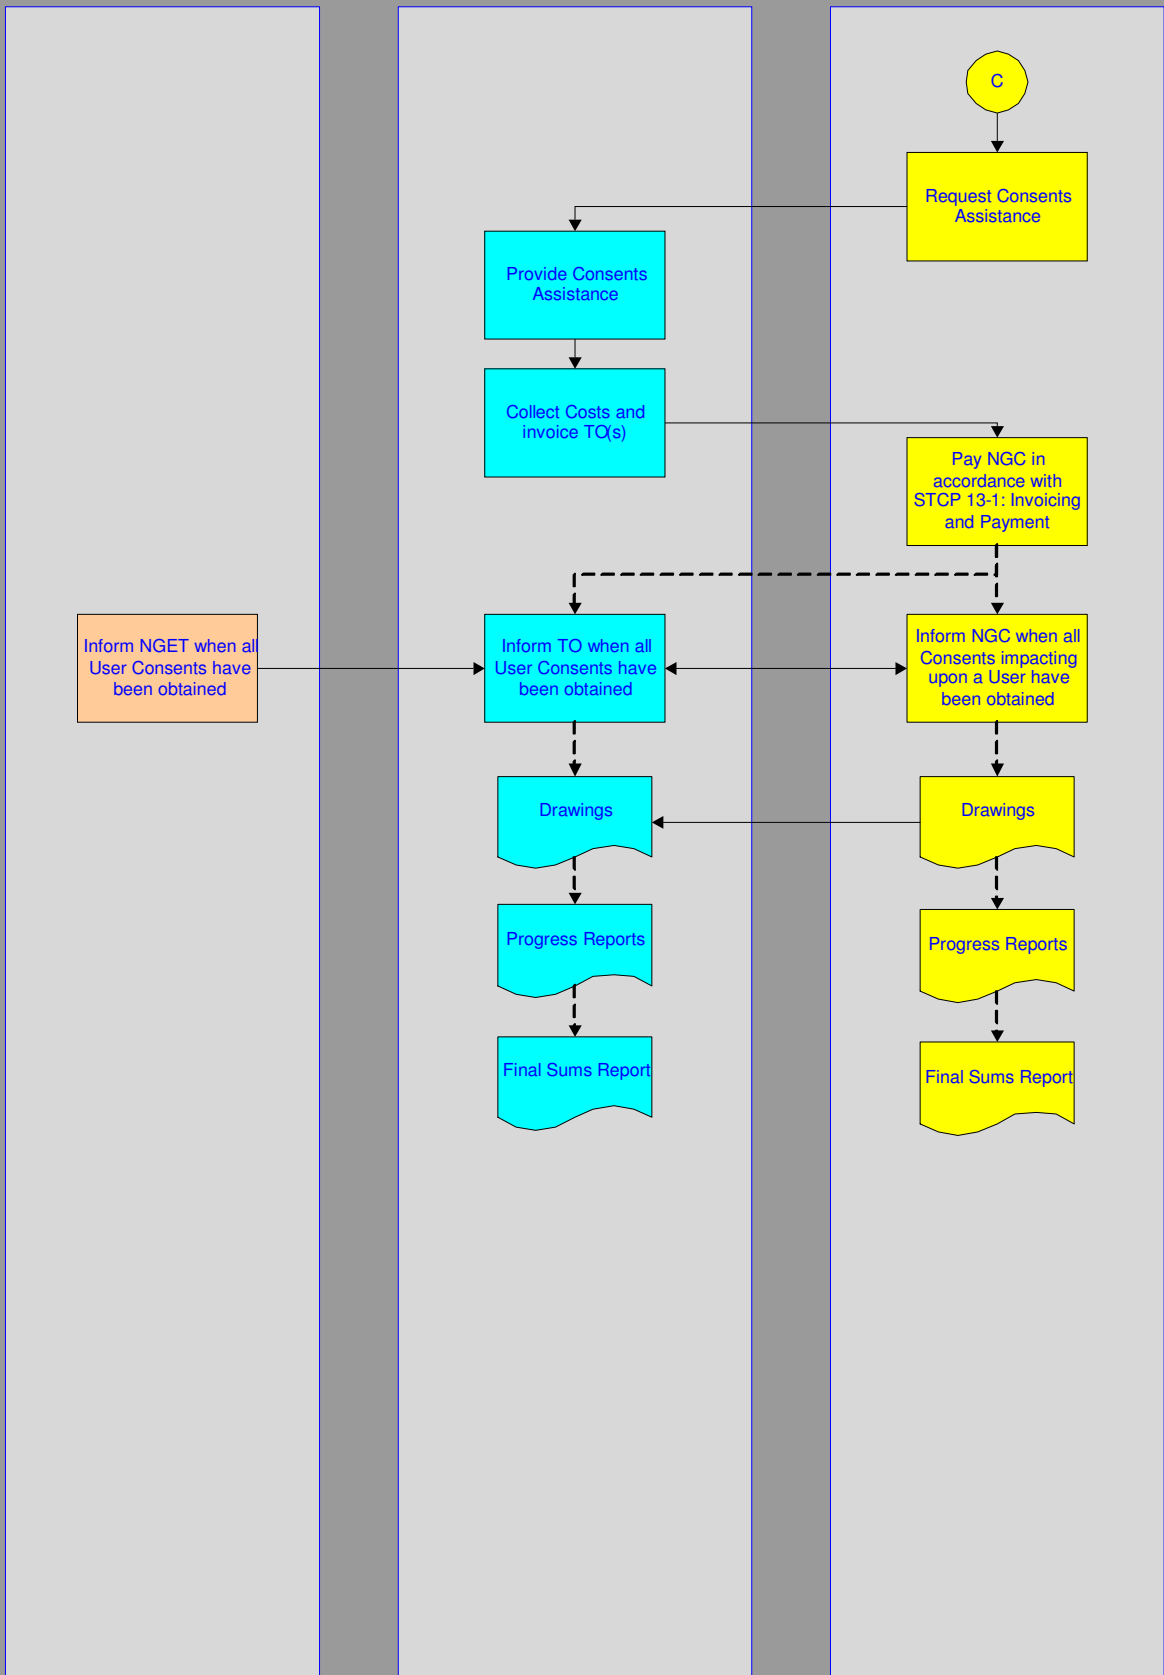


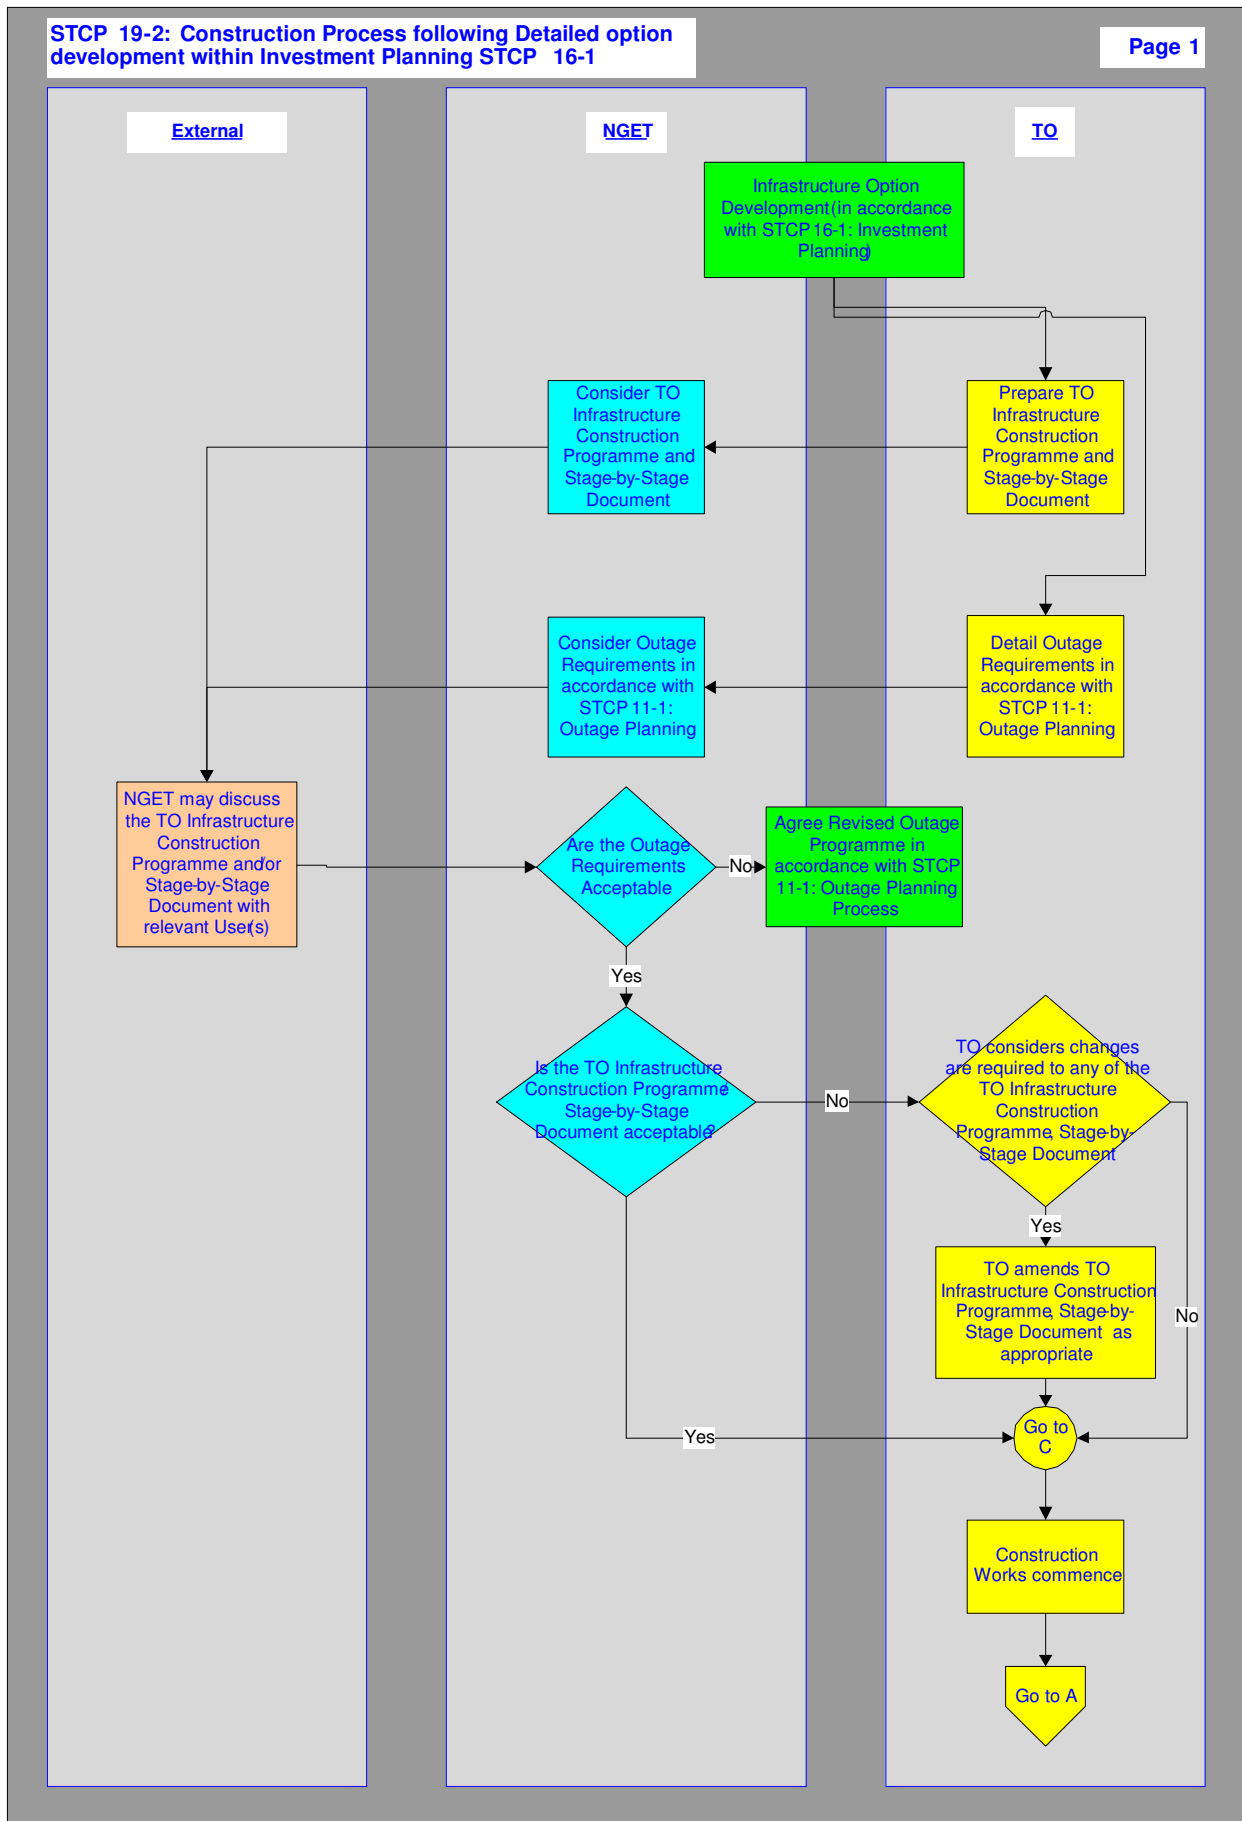


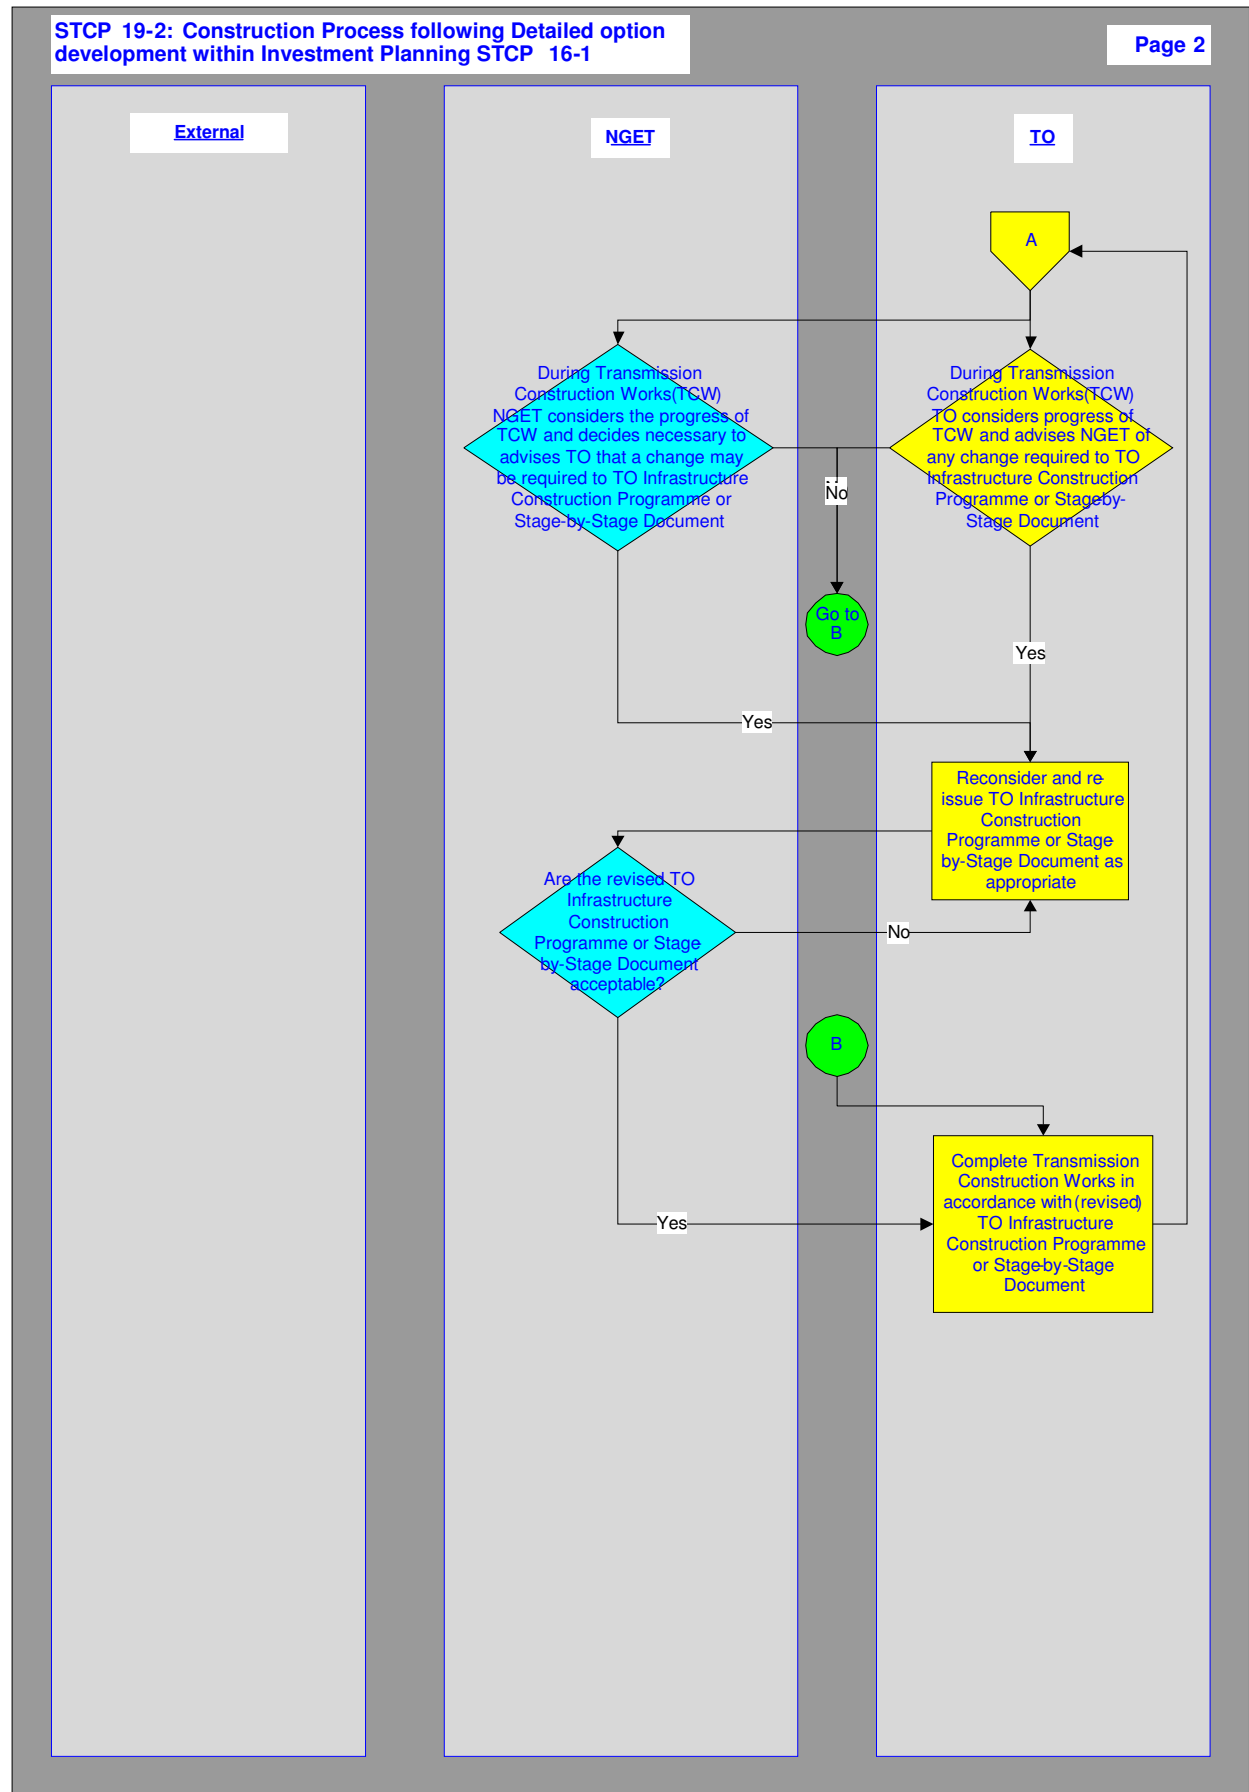


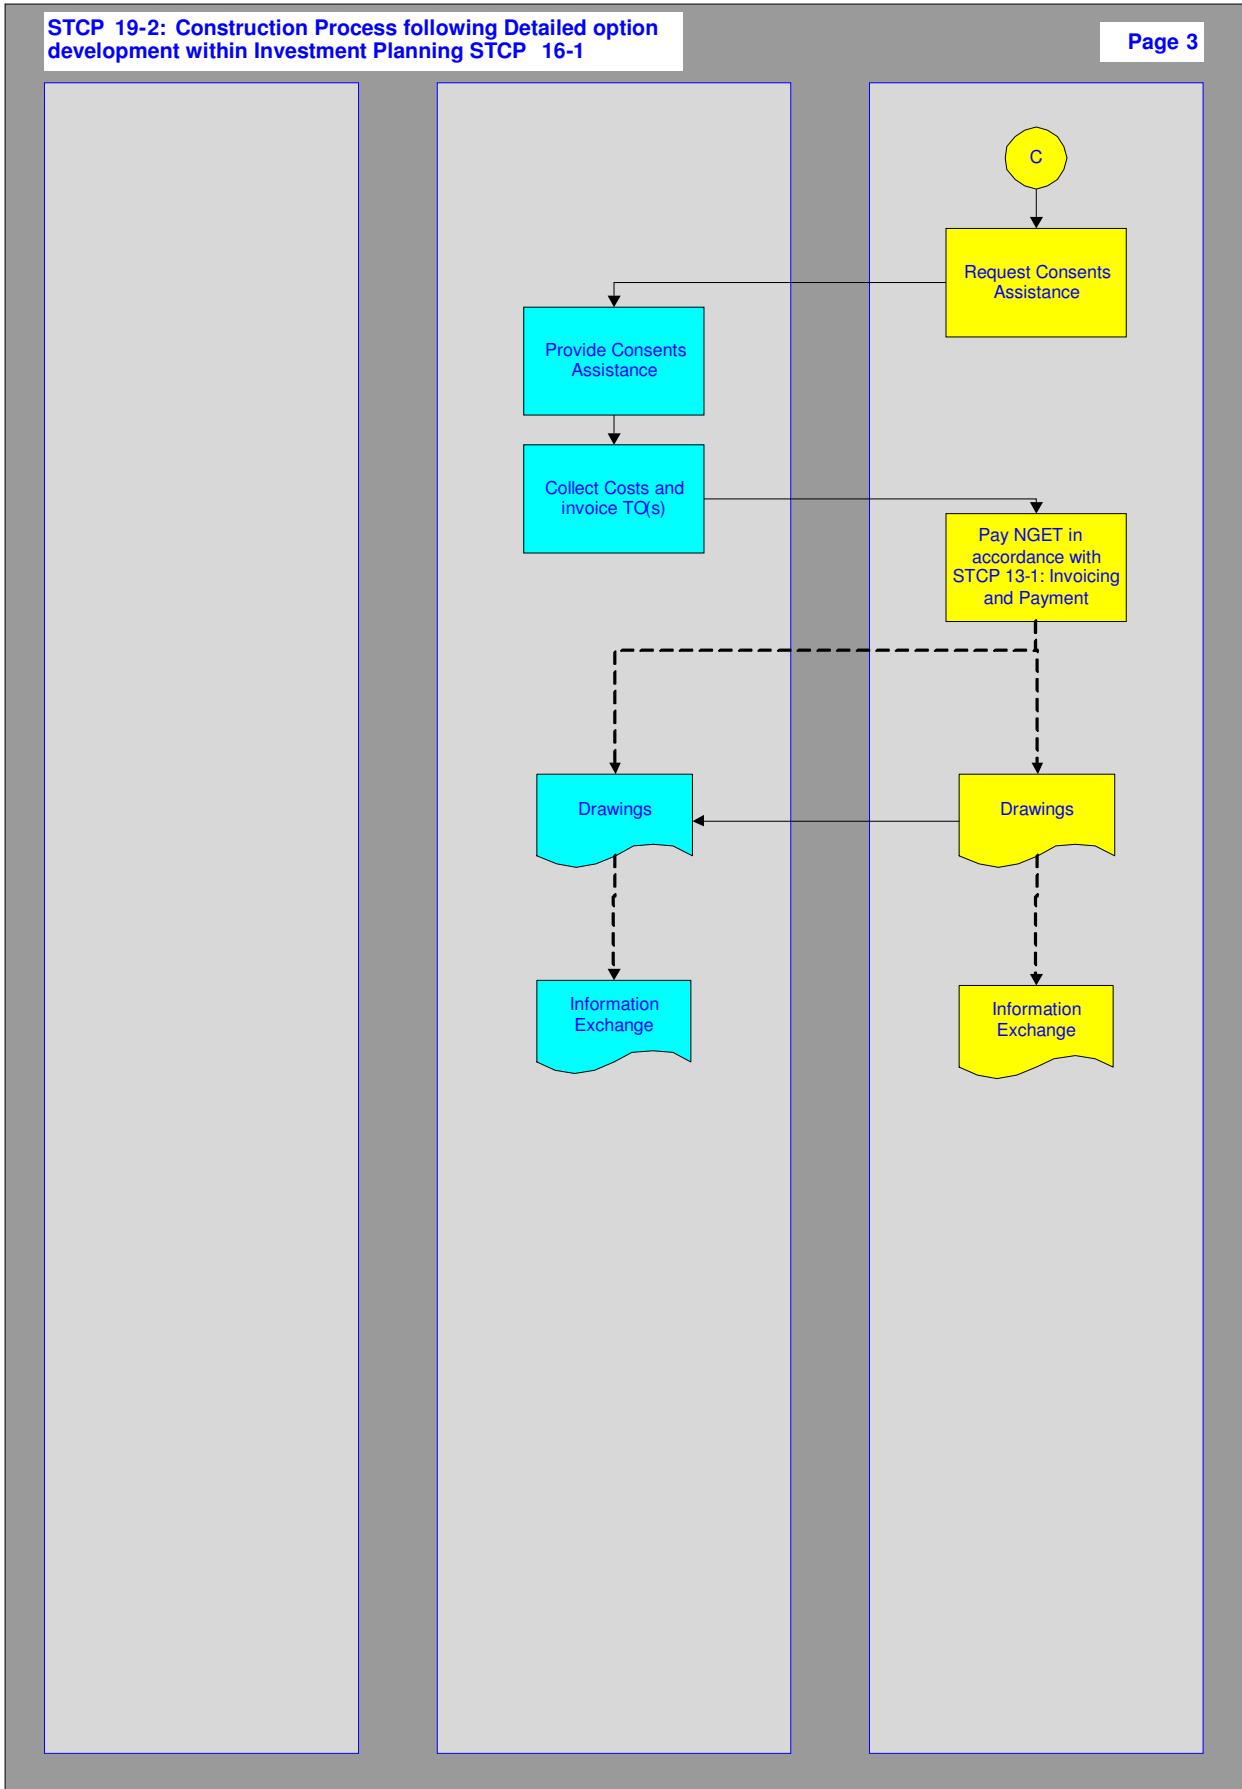


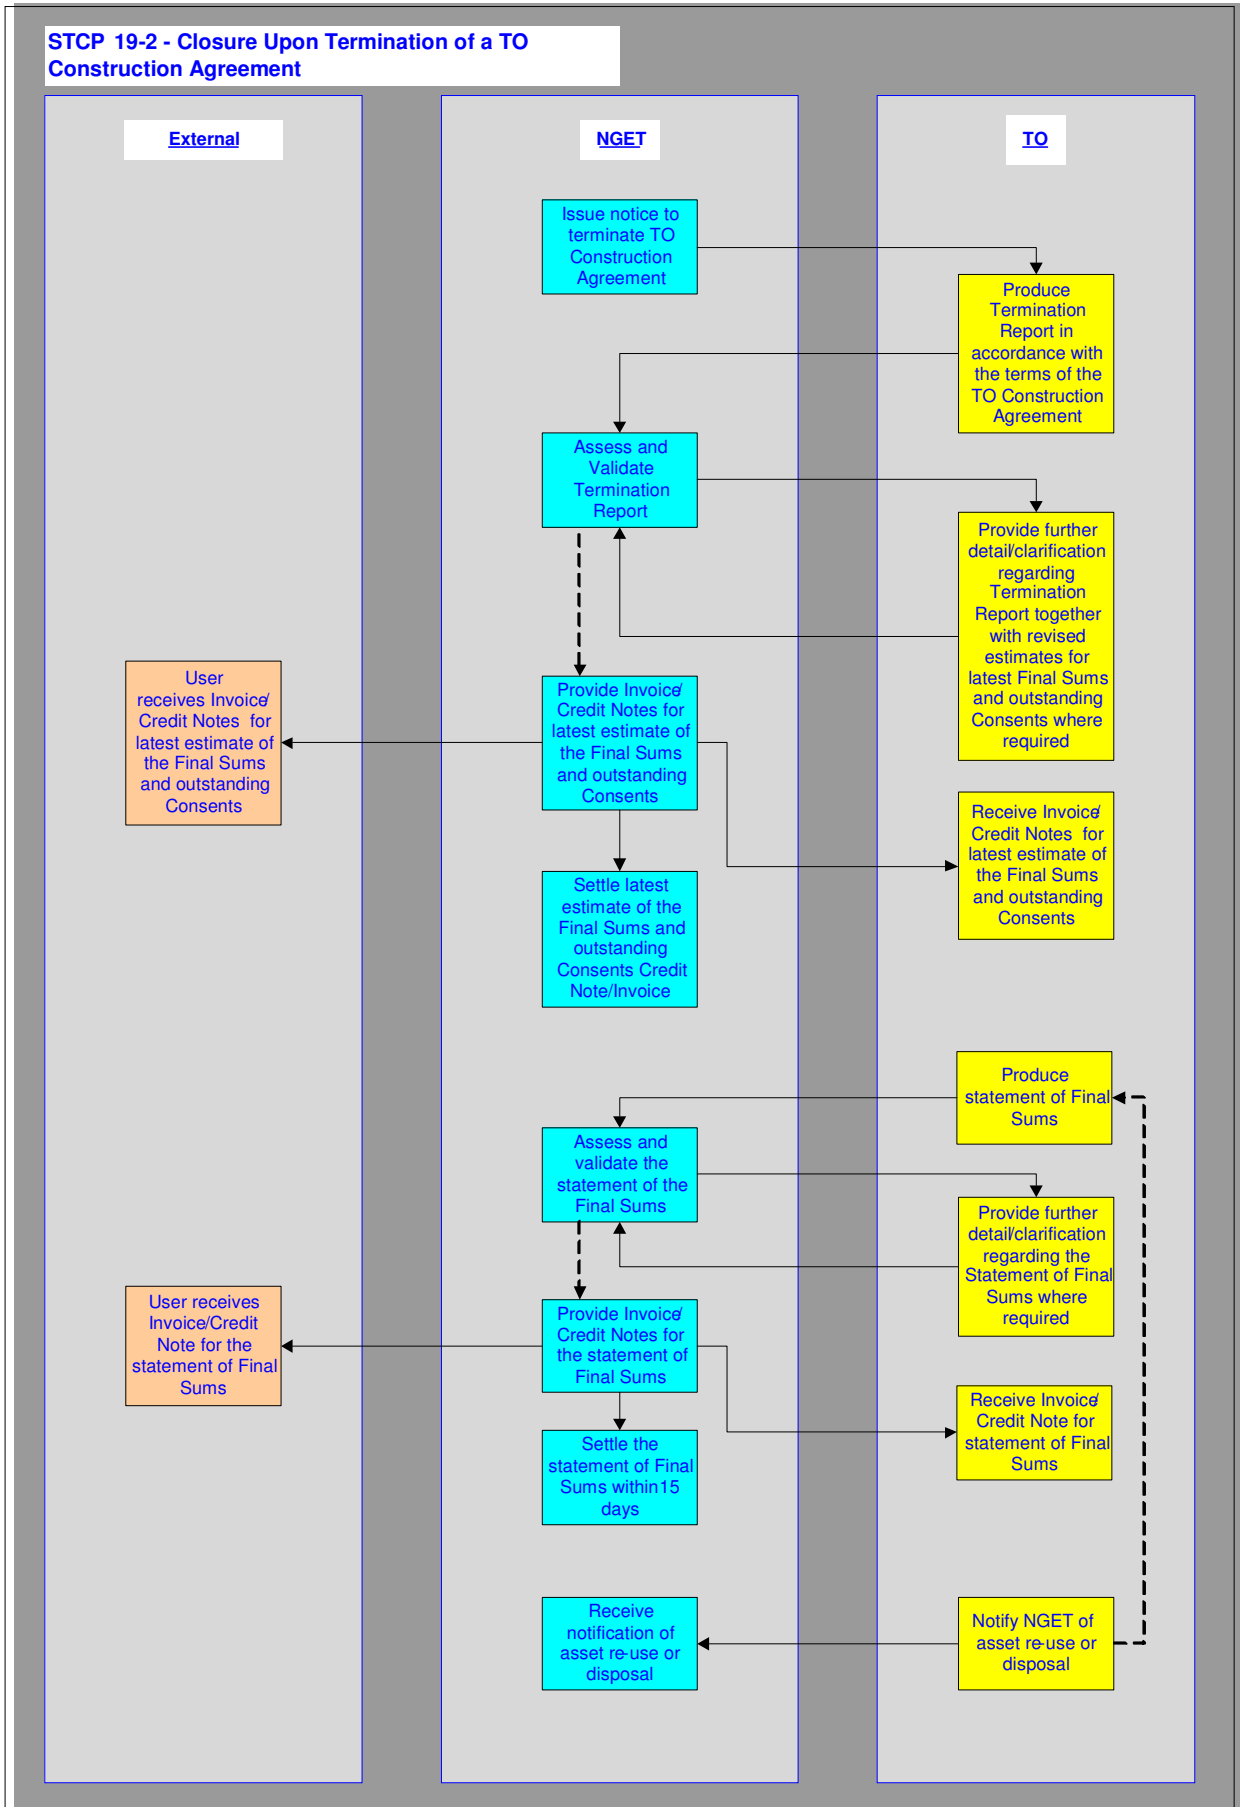

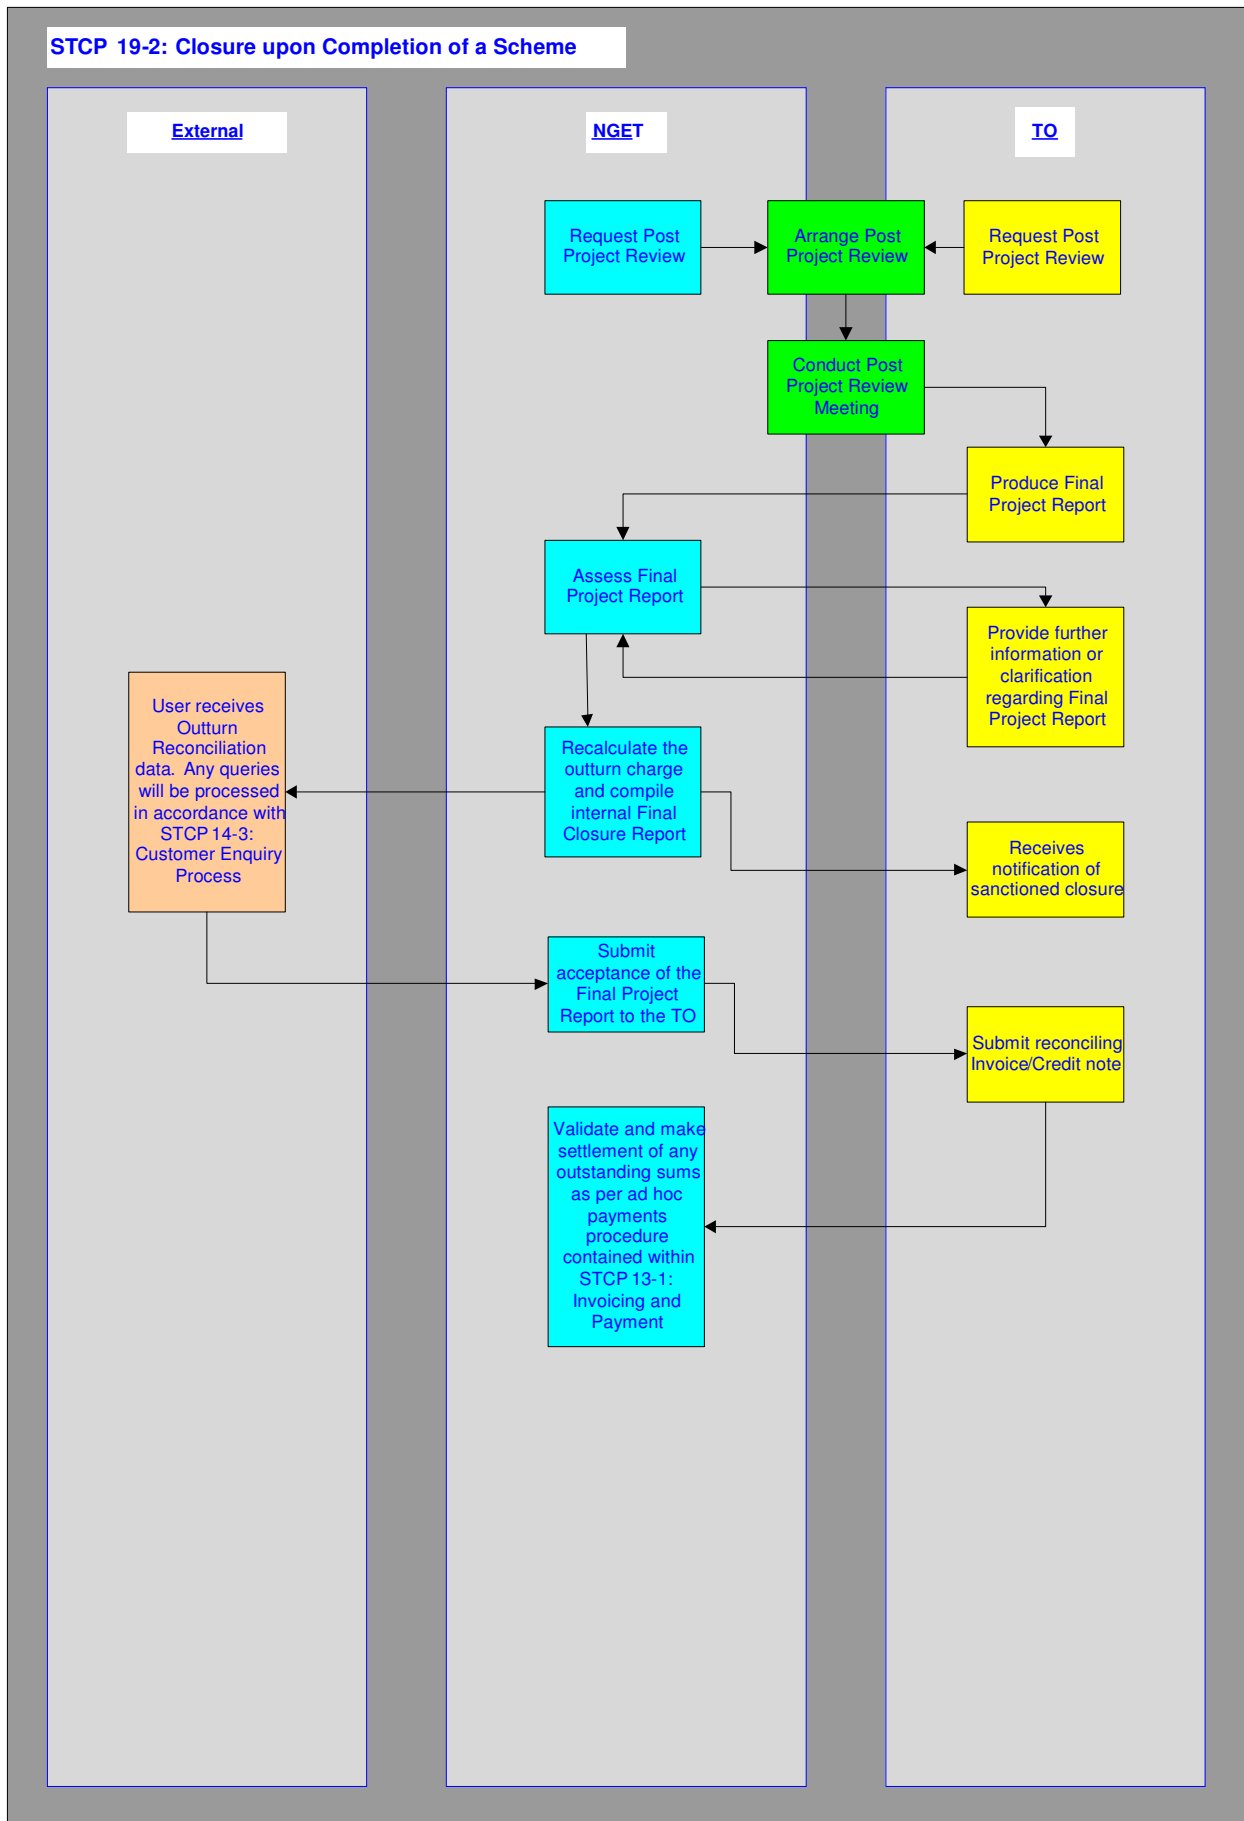

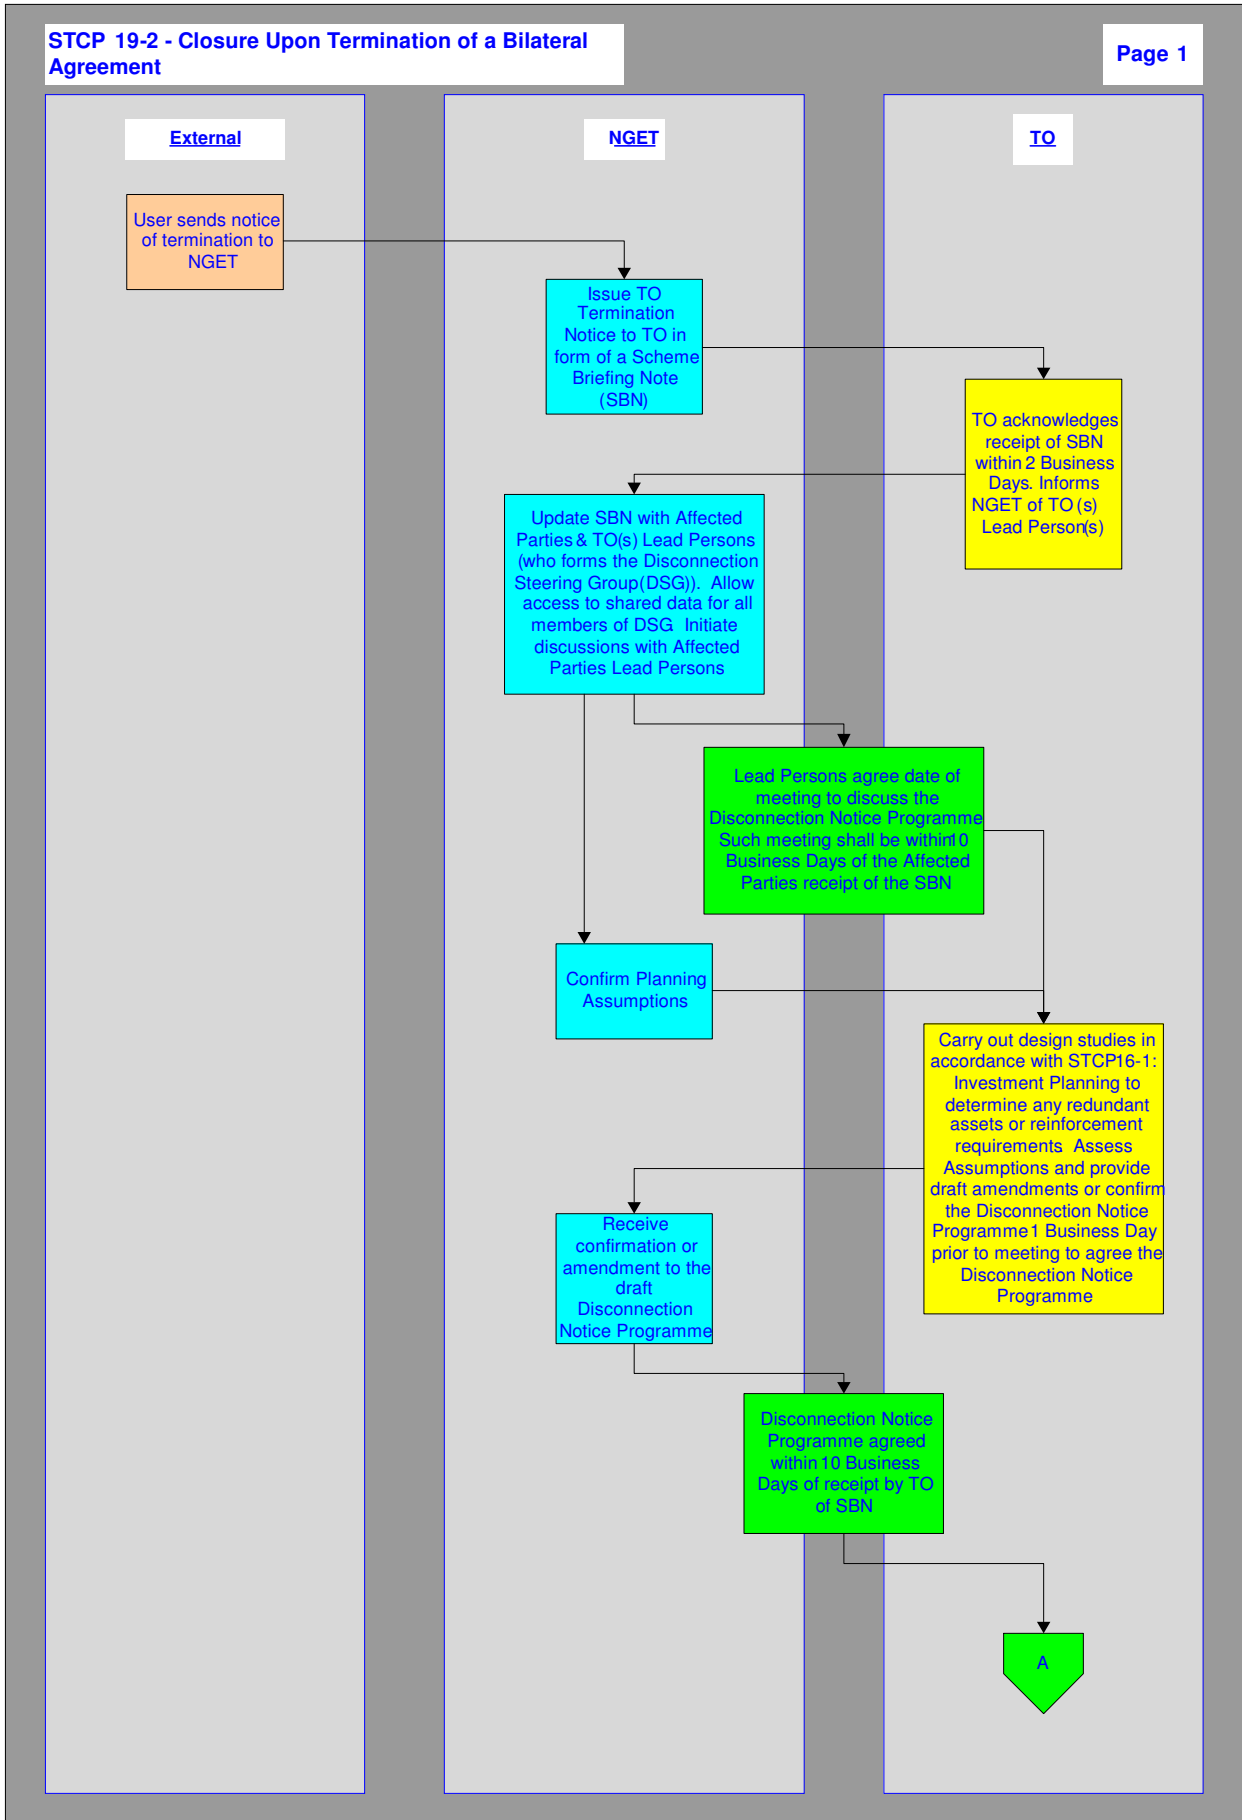

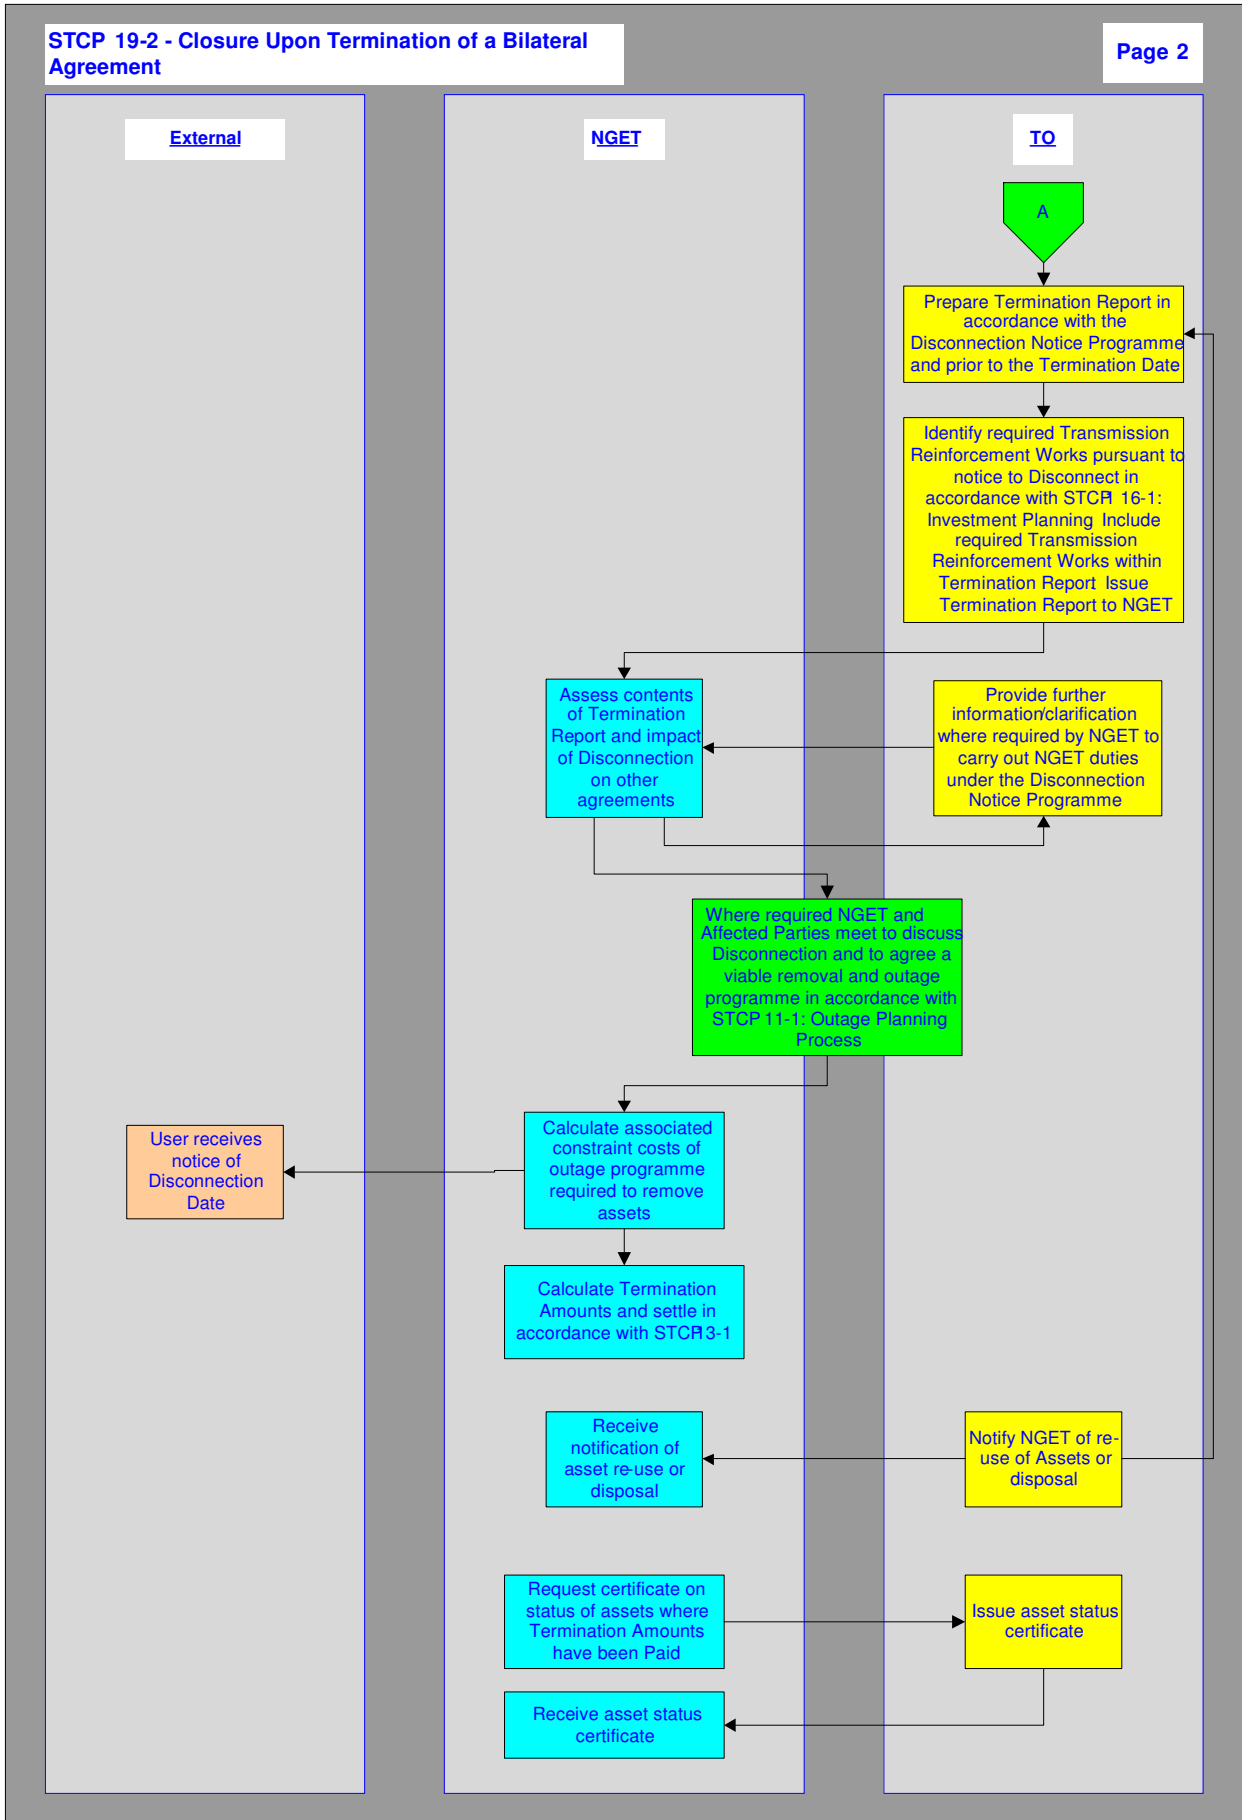

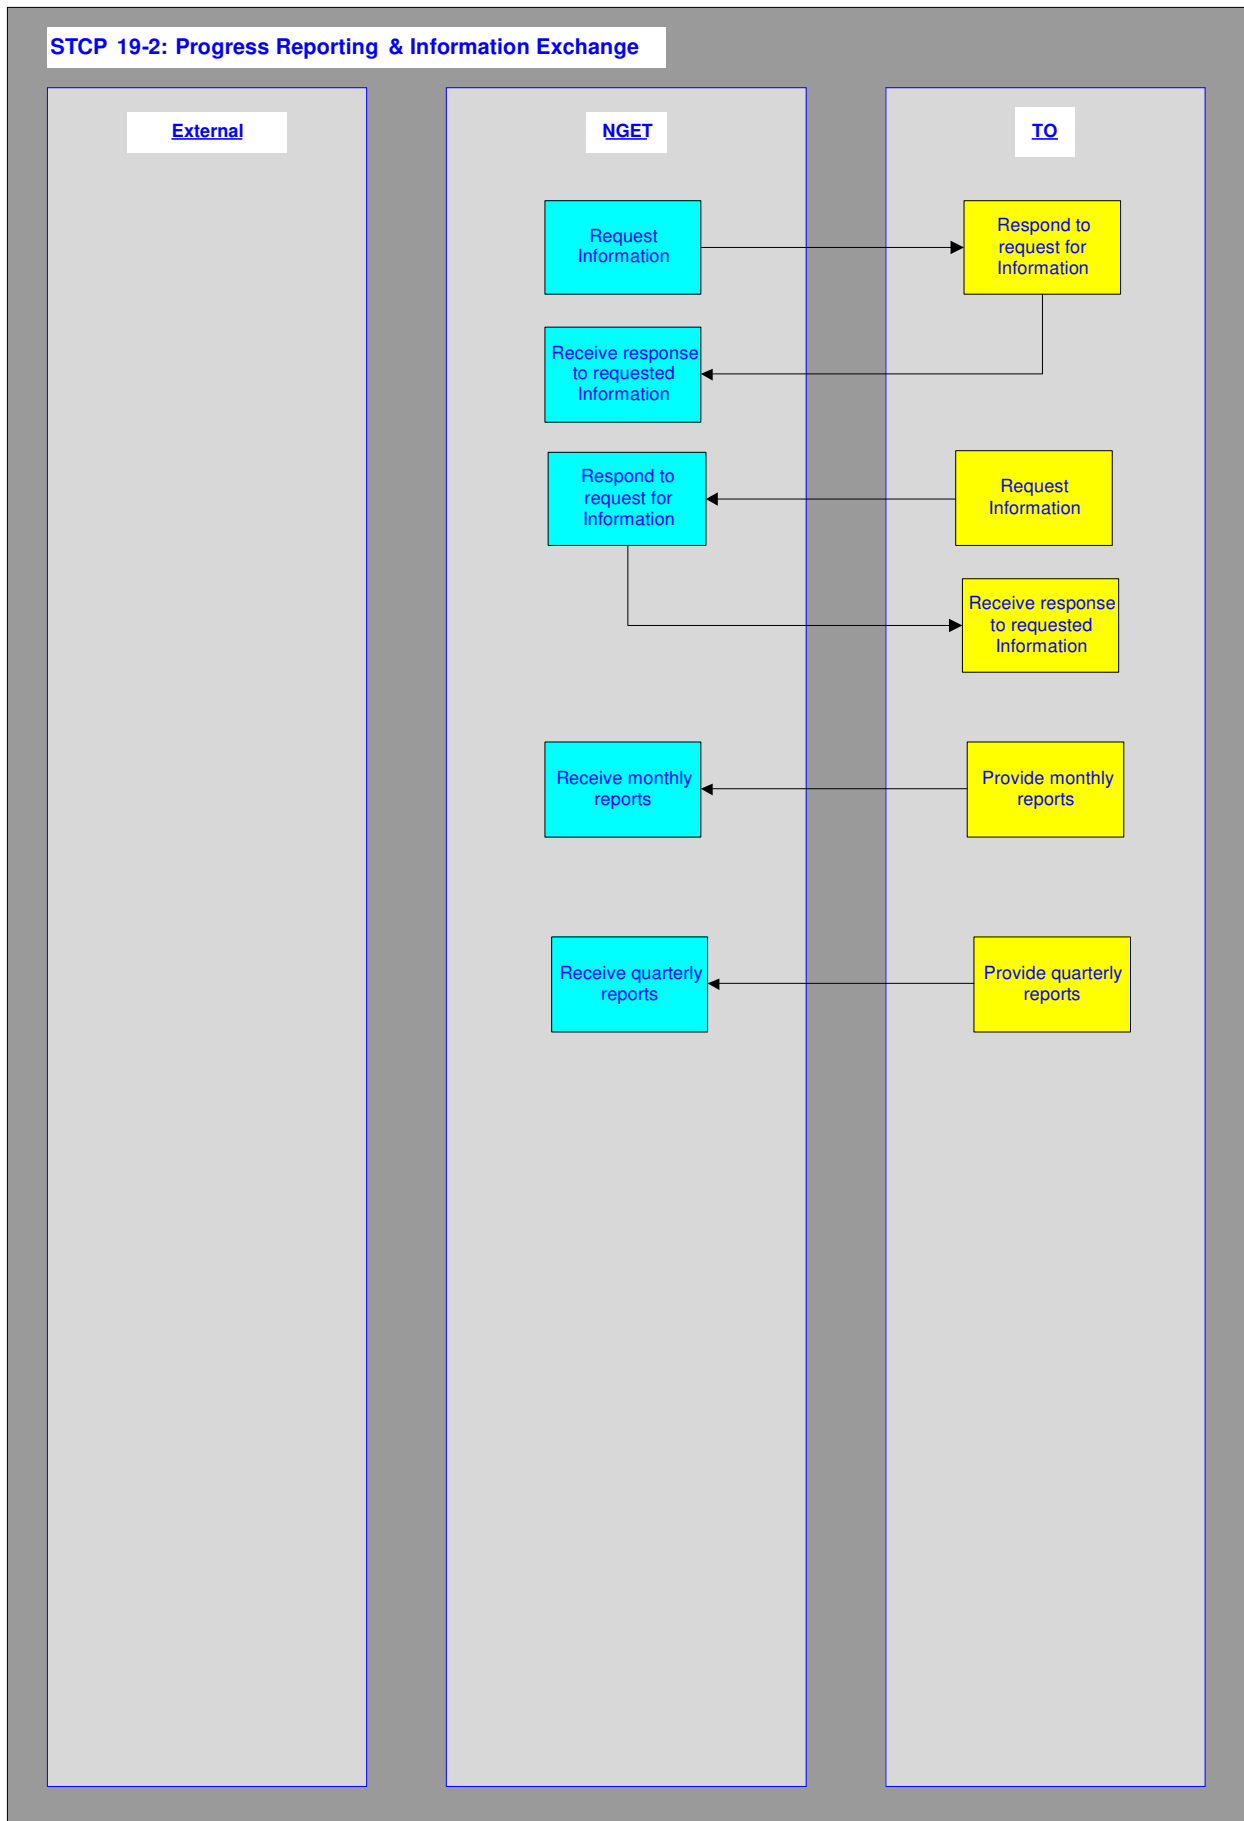

Appendix B: Consents Reporting Pro-Forma:

Consents Status Report under STCP 19-2			
To (at NGET):		User:	
From (at TO):		Site:	
Date:			
NGET scheme no:			

	A	B	C	D
Consents Detail	Value of Consents incurred to / /	Unspent Commitments	Future Commitments	Expected Total Consents (A+B+C)
	Total	Total	Total	Total
	£(ex vat)	£(ex vat)	£(ex vat)	£(ex vat)

Progress this Period

[headline summary]

Appendix C: Quarterly Reporting Pro Forma

TO:

SITE: []

CONNECTION OF: [USER]

CONTRACT REFERENCE:

Quarterly Report: [First/Second/Third/Fourth] Quarter 200[]

Switchgear and Civils (composite/other contract)

OHL Line Contract

Cable Contract

Unlicensed Work (where material to progress of Licensed Work/Impacts on Connection Date)

Programme and Consents

Bilateral Connection Agreement / TO Construction Agreement and Associated Issues

[Costs – For Indicative Priced Agreements

The costs underlying the Connection Charges set out in the Bilateral Connection Agreement dated [] have increased / decreased by approximately [%], and the Connection Charges shall be likely to change by a corresponding proportion. Similarly, the TO Final Sums liability for the remainder of the Detailed TO Construction Programme shall also change correspondingly.]

[Costs – For Firm Priced Agreements

The costs underlying the Final Sums for the Bilateral Connection Agreement dated [] have increased / decreased by approximately [%], and the Final Sums shall be likely to change by a corresponding proportion.]

Confirmation that the scope of works have not changed.

Confirmation that the programme has not changed.

Appendix D: TO Final Sums Reporting

BI-ANNUAL TO FINAL SUMS REPORT

TO:

User:

Site:

NGET Scheme No:

Amount due and amount which shall or might fall due for the period commencing on and including [xx/xx/xxxx] and ending on and including [xx/xx/xxxx].

1. Engineering Charges & expenses for obtaining Consents
2. TO Final Sums

Explanatory notes:

[To include explanation of major variances, risks, key issues etc]

Appendix E: Scheme Outturn Charge Notification

Scheme Outturn Charge Notification

Charge Basis

Users:

Agreement Reference:

Site:

Charging Date:

Year	2005/06	2006/07
Rate of Return %		
Depreciation %		
Site Specific Maintenance %		
Transmission Running Costs %		

Connection Asset	GAV in year prior to outturn	Year prior to outturn	GAV in year of outturn	Year of outturn
	@ April 2005 price	2005/06 annual charge	@ April 2006 price	2006/07 annual charge
Total	£0.00	£0.00	£0.00	£0.00

Where applicable

Outturn One-off Charge at Charging Date:	£0.00
--	-------

Appendix F: Termination Amounts Reporting

BI-ANNUAL TERMINATION AMOUNTS REPORT

TO:

User:

Site:

NGET Scheme No:

Amount due and amount which shall or might fall due for the period commencing on and including [xx/xx/xxxx] and ending on and including [xx/xx/xxxx].

1. Termination Amounts

Explanatory notes:

[To include explanation of major variances, risks, key issues etc]

Appendix G: Abbreviations & Definitions

Abbreviations

OFTO	Offshore Transmission Owner
SPT	SP Transmission Limited
SHETL	Scottish Hydro-Electric Transmission Ltd
SBN	Scheme Briefing Note
TOCA	TO Construction Agreement
TO	Transmission Owner

STC definitions used:

Calendar Quarter
Commissioning Programme Commencement Date
Completion Date
Connection
Connection Site
Connection Site Specification
Consents
Construction Project
~~GB~~-National Electricity Transmission System
Interface Agreement
Joint Project Parties
NGET
One Off Works
Outage
Planning Assumptions
Plant
Services Capability Specification
System
Transmission Connection Assets
Transmission Construction Works
Transmission Owner
TO Construction Agreement
TO Construction Programme
Transmission System
User
User Equipment

CUCS definitions used:

Bilateral Agreement
Construction Agreement
Demand
Disconnect
Disconnection
One-off Works
Termination Amount

Definition used from other STCPs:

Project Listing Document	As defined in STCP16-1: Investment Planning
Affected Parties	As defined in STCP18-1: Connection and Modification Applications
Affected TO	As defined in STCP18-1: Connection and Modification Applications
Charging Methodology	As defined in STCP14-1: Data Exchange for Annual Charge

	Setting
Host TO	As defined in STCP18-1: Connection and Modification Applications
Named Contact	As defined in STCP18-1: Connection and Modification Applications
Other Affected TO	As defined in STCP18-1: Connection and Modification Applications
Scheme Briefing Note	As defined in STCP18-1: Connection and Modification Applications
Indemnity Agreement	As defined in STCP18-1: Connection and Modification Applications
